



उत्तराखण्ड पावर कारपोरेशन लि०

(उत्तराखण्ड सरकार का उपक्रम)

Uttarakhand Power Corporation Ltd.

(A. Govt. of Uttarakhand Undertaking)

CIN : U40109UR2001SGC025867

Email ID: cgmupcl@yahoo.com, Website: www.upcl.org

Letter No. 4500 /CE(Comm1.)/UPCL

Date: 7 /07/2025

The SECRETARY
Uttarakhand Electricity Regulatory Commission
"Vidyut Niyamak Bhawan"
Near ISBT, Dehradun,

Sub: Regarding time extension of the SCoD for 2.5 MW Canal Bank Grid Connected Solar PV Project near Bridge No.1 on Yamuna Power Channel, Dakpathar.

Hon'ble Commission is humbly requested to kindly refer to UJVNL letter no. M-32/UJVNL/02/D(Operations)/GM (Comm.)/ dated 20-06-2025 (Copy enclosed) vide which it has been informed that the work of development of the aforementioned 2.5 MW Canal Bank Solar plant is being done through M/s Evolve Green Energies Private Limited and the completion period of the project was on or before 12 months from the date of the execution of the PPA and accordingly the SCOD of the plant was 18-06-2025. Also it is informed that the work of the project is not completed due to some reasons and further UJVNL has requested for time extension of further 6 months from 18-06-2025 to 18-12-2025.

The above mentioned Solar Power plants of cumulative capacity 2.5 MW and of intermittent nature and shall be generating only during the normal hours so as such the delay in the commissioning of this plant doesnot have any significant impact on the power procurement portfolio of UPCL.

Further, it is also worthwhile to mention that in accordance with the UERC (Tariff and Other Terms for Supply of Electricity from Renewable Energy Sources and non-fossil fuel based Co-Generating Stations) (First Amendment) Regulations, 2024 , all the Renewable Energy Generators including Solar Generators having capacity less than 10 MW will contribute towards the fulfillment of Distributed RPO and as per the target specified by Hon'ble UERC for FY 2025-26, the delay in commissioning of these this project will not impact the fulfillment of The Distributed RPO as it is being achieved with the energy being generated from the current renewable energy generators having capacity below 10 MW.





उत्तराखण्ड पावर कारपोरेशन लि०
(उत्तराखण्ड सरकार का उपक्रम)
Uttarakhand Power Corporation Ltd.
(A. Govt. of Uttarakhand Undertaking)
CIN : U40109UR2001SGC025867
Email ID: cgmupcl@yahoo.com, Website: www.upcl.org

Therefore in light of the aforementioned facts, UPCL is of the view that a six month extension may be given to UJVN Ltd. for the commissioning of 2.5 MW Canal Bank Grid Connected Solar PV Project near Bridge No.1 on Yamuna Power Channel, Dakpathar.

In view of the above, Hon'ble Commission is humbly requested for further necessary order in the matter.


Encl: As above.


(D.S.Khati)
Chief Engineer (Commercial)

Letter No. /CE(Comm1.)/UPCL Date: /07/2024

Copy forwarded to following for kind information in the matter:

1. SO-I to Managing Director, UPCL, V.C.V.G.S. Urja Bhawan, Kanwali Road, Dehradun.
2. Director (Project), UPCL, V.C.V.Gabar Singh Urja Bhawan, Dehradun.


(D.S.Khati)
Chief Engineer (Commercial)



(उत्तराखण्ड सरकार का उपक्रम)
UJVN LIMITED

(A Govt. of Uttarakhand Enterprise)

कार्यालय महाप्रबन्धक(वाणिज्य), "उज्जवल", महारानीबाग, जी०एम०एस० रोड, देहरादून- 248 006 (उत्तराखण्ड), दूरभाष: 0135-2763286, फ़ैक्स: 0135-27619
Office of the General Manager (Commercial), "UJJWAL", Maharani Bagh, G.M.S. Road, Dehradun - 248 006 (Uttarakhand), Phone: 0135-2763286, Fax: 0135-2761955
CIN No. 40101UR2001SGC025866, ISO 9001:2008 Certified

No. M-32 /UJVNL/02/Director (Operations)/GM(Comm.)/

Date: 20/06/2025

Chief Engineer (Commercial)
Uttarakhand Power Corporation Limited
VCV Gabar Singh, Ujra Bhawan
Kanwali Road, Dehradun.

Sub: Regarding time extension of 2.5 MW Canal Bank Grid connected Solar PV Project near bridge No.1 on Yamuna Power Channel, Dakpathar.

On the above cited subject, it is to inform that a PPA dated 19.06.2024 was executed between UJVNL and UPCL for 2.5 MW Canal Bank Grid-connected Solar project situated on Yamuna Power Channel near Bridge No. 01, Dakpathar Barrage; District-Dehradun. The work of development of the aforesaid Solar PV is being done through M/s Evolve Green Energies Private Limited (Formerly M/s Shimato Enterprises Private Limited). The scheduled completion period of the project was on or before 12 months from the date of execution of PPA. Accordingly, The SCOD of the plant is 18/06/2025.

In this regard, it is to inform that above work have not been completed yet due to some reason and developer has requested for time extension of further six months from 18.06.2025 to 18.12.2025.

In view of the above, the detailed report along with relevant documents are being submitted with request that six-month time extension against aforesaid PPA may kindly be allowed for completion of the project & the confirmation of the same may kindly be conveyed at the earliest.

(K. K. Jaiswal)
General Manager (Commercial)

Encl. As above

Copy to following for kind information –

1. Director (Operations), "UJJWAL", UJVN Ltd., Maharani Bagh, Dehradun.
2. Director (Projects), "UJJWAL", UJVN Ltd., Maharani Bagh, Dehradun.

Report on Proposal for Time Extension of 2.5 MW Canal Bank Grid-Connected Solar PV Project at Dakpathar, Dehradun

2.5 MW Canal Bank Grid-Connected Solar PV Project is being developed on the Yamuna Power Channel near Bridge No. 01, Dakpathar, District Dehradun through M/s Evolve Green Energies Private Limited (formerly M/s Shimato Enterprises Private Ltd) under the BOOT (Build, Own, Operate, Transfer) model. For this project, UJVNL has signed a Power Purchase Agreement (PPA) with Uttarakhand Power Corporation Limited (UPCL) on 19.06.2024 for the sale of energy generated from the 2.5 MW solar plant. Subsequently, UJVNL also entered into PPA with the solar power developer on 07.08.2024 for purchase of power.

As per the PPA signed between UJVNL and UPCL, the scheduled commissioning period for the project is **twelve (12) months from the date of signing** of the UPCL–UJVNL PPA. Accordingly, the scheduled date of commissioning of the project is **18.06.2025**. The PPA between UJVNL and the solar developer also aligns with this schedule.

According to the progress reports submitted by the developer and request letter no. SEPL/TRPR/UJVNL/2.5MW/TR-22 dated 27.05.2025 (**copy enclosed**), substantial work has been undertaken at the site. The retaining wall along the canal has been constructed. Land levelling has been carried out in all accessible areas except those impacted by encroachments and standing trees. Fencing work is also completed except in encroached portions. In addition, the developer has procured solar modules and inverters, which are ready for dispatch and installation. However, critical obstacles over the timeline have stalled further progress.

The following issues have significantly affected the project timeline:

1. **Encroachment on Project Land:**

A portion of the allocated land remains encroached by local residents, preventing full site access and the finalization of the layout for civil and electrical works. The matter has been escalated to the local administration, and UJVNL has formally requested the SDM, Vikasnagar for police support to ensure safe and timely removal of encroachment to facilitate project execution. (**copy enclosed**)

2. **Tree Removal Pending Clearance:**

Several trees are located within the proposed project layout. Although the necessary tender for tree removal was floated, work has not commenced due to the time taken in obtaining requisite Forest Deptt. approvals. UJVNL has made multiple submissions and follow-ups with the Forest Department for early clearance of the proposal, including submission of all required technical documents and site maps. (**copy enclosed**)

For G1

ag
2024

Despite the efforts made by UJVNL and the developer, these factors being outside the control of the solar developer have resulted in project delays. M/s Evolve Green Energies Private Limited has mobilized men and material and is ready to proceed with installation. However, until encroachment is cleared, and tree removal is completed, further development is not possible.

In this context, the developer has formally requested a **six-month extension** in the project completion timeline, from 18.06.2025 to 18.12.2025. Further, it is pertinent to mention that the solar developer, M/s Evolve Green Energies Private Limited, has submitted a No Claim Certificate, wherein they have categorically affirmed that they shall not raise any claim for compensation, damages, or financial adjustment of any kind due to the grant of this extension. They have also undertaken not to seek any enhancement in the interest or value of the contract bond for the work executed during the extended period. This declaration provides an assurance that UJVNL shall bear no financial liability on account of the proposed extension.


Current Status:

1. UJVNL is working judiciously with local administration for removal/demolition of encroachment from its land and handover to solar developer. The matter is being perused with administration by Civil and Solar Deptt. for early disposal of the matter.
2. After obtaining due approval from the Forest Deptt. for cutting of trees on the subject land, the work of cutting of trees has been awarded by Civil Wing on 28.05.2025 through open tender basis. The cutting of trees is scheduled to be completed by 21.06.2025.

In view of above, it is evident that time extension has been sought for reasons not attributable to the solar developer. It is important to note that UJVNL can only grant such an extension to the solar developer **after obtaining corresponding approval from UPCL**, since the PPA between UJVNL and UPCL also defines 18.06.2025 as the project commissioning deadline. Without UPCL's approval, any amendment to the commissioning schedule would constitute a deviation from the existing agreement terms. Once such approval is received from UPCL, UJVNL will accordingly grant a corresponding extension to the developer.

In light of the above, it is recommended for accord of approval for time extension in the 2.5 MW Canal Bank Grid-Connected Solar PV Project commissioning timeline from 18.06.2025 to 18.12.2025 (six months) for reasons enumerated above being not attributable to the Solar Developer.

Encl.: As above


(S. N. Prajapati)
Executive Engineer (Solar)


(Bharat Bharadwaj)
Dy. G. M. (Solar, MM&CM)

Ref No: SEPL/TRPR/UJVNL/2.5MW/TR-22

27-05-2025

To,
The Executive Engineer (Solar),
UJVNL Limited,
"Ujjwal", Maharani Bagh,
GMS Road, Dehradun-248006.

Subject: Request for Extension of Project Completion Timeline - 2.5 MW Canal Bank Solar PV Project, Dakpathar, Dehradun

Respected Sir,

Ref:

1. Our Request Letter Ref. No. Nil (Tree Cutting Work), dated 24.12.2024
2. Our Request Letter Ref. No. Nil (Existing Transmission line & Transformer Shifting), dated 24.12.2024
3. Your Letter Ref. No. Nil, dated 26.12.2024
4. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/LR-05, dated 27.12.2024
5. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-08, dated 07.03.2025
6. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-12, dated 19.03.2025
7. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-13, dated 25.03.2025
8. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-15, dated 03.04.2025
9. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-16, dated 03.04.2025
10. Your Letter Ref. No. 82/UJVNL/EE(Solar), dated 05.04.2025
11. Your Letter Ref. No. 84/UJVNL/Superintendent (Solar), dated 05.04.2025
12. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-17, dated 17.04.2025
13. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-18, dated 23.04.2025
14. Your Letter Ref. No. 97/UJVNL/EE(Solar), dated 24.04.2025
15. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-19, dated 02.05.2025
16. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-20, dated 17.05.2025

We are writing to provide an update on the progress of the 2.5 MW Canal Bank Grid-Connected Solar PV Plant project on the Yamuna Power Channel near Bridge No. 01, Dakpathar, District Dehradun. This update is in accordance with the Letter of Intent (LOI) No. B-51/UJVNL/EE(Solar) dated 17.02.2024 and the Power Purchase Agreement (PPA) signed on 07.08.2024. Additionally, we seek your kind approval for a six-month extension to the project completion timeline due to unforeseen challenges beyond our control.

Work Progress Update:

1. The retaining wall construction has been successfully completed.
2. Fencing work is complete, except in areas affected by encroachments and existing trees.
3. Land leveling is complete, except in areas with encroachments and trees.

Reasons for Delay:

Despite our diligent efforts, the project has faced significant delays due to the following issues:

1. **Encroachment Issues:** Residents have not vacated the proposed solar installation area allocated by M/s. UJVNL, hindering site preparation and layout finalization.
2. **Tree Cutting Delays:** Although M/s. UJVNL floated a tender for tree cutting, the work has not yet commenced, further delaying site clearance.

Despite the challenges faced, we have made the following progress at the site:

1. Completed construction of the retaining wall.
2. Finished land leveling, excluding areas with encroachments and trees.
3. Installed fencing, except in areas affected by encroachments and existing trees.

We have also submitted the Land Memorandum of Understanding (MoU) documents to M/s. UJVNL; however, the documents have not yet been signed by M/s. UJVNL. Additionally, the demarcation process was completed only on 14th May 2025 by government officials, which has further impacted the project timeline.

Solar modules and inverters are readily available with us for dispatch; however, we have been unable to proceed with material supply to the site due to the unresolved issues related to land encroachment and tree removal. We have submitted multiple requests to M/s. UJVNL for land allocation free of encroachment and for the removal of trees at the proposed site, but these matters remain pending.

Request for Extension:

In view of these unforeseen circumstances, we respectfully request a six (6) month extension to the project completion timeline, effective from 18-06-2025. We further request that no penalties be levied, as the delays are attributable to factors beyond our control. This extension will enable us to deliver a high-quality project that aligns with the tender's technical standards.

We deeply appreciate your continued support and cooperation and kindly urge your favorable consideration of this request.

Thank you for your understanding and support. We look forward to your positive response.

For Evolve Green Energies Private Limited,


Authorized Signatory

Enclosed: 1) Application for extension of time part-I

2) Correspondence letter communications.

**APPLICATION FOR EXTENSION OF TIME PART-I
(TO BE SUBMITTED BY THE SOLAR DEVELOPER)**

Setting-up of 2.5MW(AC) Canal Bank Grid Connected Solar
PV Plants on Yamuna Power Channel Near Bridge No-1,
Dakpathar District - Dehradun, Uttarakhand, On Build, Own,
Operate & Transfer (BOOT) basis for UJVNL in the State of
Uttarakhand

Certificate No.: IN-UK36527064669445W,
Date: 05-08-2024

19-06-2024

18-06-2025

Nil

16-12-2025

Letter Attached
Ref No: SEPL/TRPR/UJVNL/2.5MW/TR-22

Name of Work: -

Agreement No. & Date: -

Date of start as per agreement: -

Date of Completion as per agreement/ or extended already: -

Date to which extension has been applied last but not
sanctioned: -

Date up to which extension is now applied for: -

Detailed reasons for extension is being applied for

(Fill in here or attached letter)

Application Attached

No Claim certificate by the contractor / Solar Developer

Certified that I shall not claim any compensation whatsoever due to the grant of this extension nor claim any increase in the
amount entered in my contract bond for the works done to extend the extended period.



Signature of Contractor

Address: -

No.371, SIDCO Industrial Estate,
NP) Ambattur, Chennai-600098

To,
The Executive Engineer (Solar)



Ref No: SEPL/TRPR/UJVNL/2.5MW/TR-24

29-05-2025

To,
The Executive Engineer (Solar),
UJVN Limited,
"Ujjwal", Maharani Bagh,
GMS Road, Dehradun-248006.

Subject: Material Procurement Details – 2.5 MW Canal Bank Grid-Connected Solar PV Plant

Respected Sir,

With reference to LOI No. B-51/UJVNL/EE(Solar) dated 17.02.2024 and the Power Purchase Agreement (PPA) signed on 07.08.2024 for the 2.5 MW Canal Bank Grid-Connected Solar PV Plant on the Yamuna Power Channel near Bridge No-01, Dakpathar, District Dehradun, Uttarakhand, we are writing to inform you of the following:

We have procured the required Solar Modules and Inverters for the project. As a precautionary safety measure, these materials are currently stored at our Chennai Warehouse. Once the site clearance process is completed, we will deliver the materials to the project site.

For your kind reference, please find attached the following documents:

- Solar Module Proforma Invoice
- Inverter Order Acknowledgement Note (OAN)

Note:

- Required Solar Modules for the Project: 585 Wp – 5,824 nos.
- Required On-Grid Inverters for the Project: 350 kW – 7 nos.

For Evolve Green Energies Private Limited,



Authorized Signatory

EVOLVE GREEN ENERGIES PRIVATE LIMITED (formally known as M/s. SHIMATO ENTERPRISES PRIVATE LIMITED)

ISO 9001 :2015, 14001 :2015 & OHSAS 18001 :2007 CERTIFIED COMPANY, NSIC & SSI / MSME Registered Company

STIN: 33AAPCS2173L1ZZ | CIN: U74990TN2011PTC078851

24.12.2024

To,

The Executive Engineer(Solar),
UJVN Limited,
"UJJWAL" GMS Road, Maharani Bagh,
Dehradun-248006.

Respected Sir,

Sub: Requesting Support for Tree-Cutting Approvals in the canal banks of 2.5 MW Canal Bank Grid Connected Solar PV Plants.

With reference to the LOI No: B-51/UJVNL/EE (Solar) / Dated:17.02.2024 & subsequent PPA signed on 7th of August 2024 for Setting-up of 2.5 MW Canal Bank Grid Connected Solar PV Plants on Yamuna Power Channel Near Bridge No-1, Dakpathar District- Dehradun, Uttarakhand.

We kindly seek your urgent intervention and support in facilitating the required Approvals for Cutting of total Trees of 250Nos which comprises of 68 Nos(Bakin -3, Kakat-15, Shesham-7, Gulmohar-11, SILVER-28, Siras-3, Mango-1) in North Side of the Site and 182Nos of Trees (Lyptus-109, Kokat-13, Silver-31, Sheesham-2, Shirish-3, Bakain-3, Kathal-2, Mango-3 & Others-16) in the South side of the Site. Which will enable us to commence construction activities without any delays.

We sincerely look forward to your positive response and swift action on this matter.

Thanks & Regards,



5

SHIMATO ENTERPRISES PRIVATE LIMITED

AN ISO 9001:2015, 14001:2015, & OHSAS 18001:2007 CERTIFIED COMPANY, NSIC & SSI / MSME Registered Company

GSTIN: 33AAPCS2173L1ZZ

24.12.2024

To,

The Executive Engineer(Solar),
UJVN Limited,
"UJJWAL" GMS Road, Maharani Bagh,
Dehradun-248006.

Respected Sir,

Sub: Requesting Support for 11kV Transmission Line & Transformer.

With reference to the LOI No: B-51/UJVNL/EE (Solar) / Dated:17.02.2024 & subsequent PPA signed on 7th of August 2024 for Setting-up of 2.5 MW Canal Bank Grid Connected Solar PV Plants on Yamuna Power Channel Near Bridge No-1, Dakpathar District- Dehradun, Uttarakhand.

We kindly seek your urgent intervention and support in facilitating the required Approvals for removal of 11kV transmission line and Transformer inside the Land allotted for us for setting of the Solar PV Plants.

We sincerely look forward to your positive response and swift action on this matter.

Thanks & Regards,

**SHIMATO ENTERPRISES PRIVATE LIMITED**

AN ISO 9001:2015, 14001:2015, & OHSAS 18001:2007 CERTIFIED COMPANY, NSIC & SSI / MSME Registered Company

GSTIN: 33AAPCS2173L1ZZ



(उत्तराखण्ड सरकार का उपक्रम)
UJVNL LIMITED

(A Govt. of Uttarakhand Enterprise)

कार्यालय—अधिशाली अभियन्ता (सोलर), "उज्ज्वल", महारानी बाग, जी०एम०एस० रोड, देहरादून-248006 (उत्तराखण्ड), दूरभाष: 0135-2761484, फैक्स: 0135-2763506
Office of the Executive Engineer (Solar), "Ujjwal", Maharani Bagh, G.M.S. Road, Dehradun-248006 (Uttarakhand), Phone: 0135-2761484, Fax: 0135-2763506
CIN No. 40101UR2001SGC025866
ISO 9001:2015, ISO 14001:2015 & 45001:2017 Certified

Date: 26-12-2024

Subject:- Regarding Tree cutting approval in land of 2.5 MW Canal Bank Solar PV Plant at Bridge no-1 Dakpathar.

Executive Engineer (Civil)
Dhalipur.
Dehradun.

Please find attachment the Solar Developer M/s Shimato Enterprises Pvt. Ltd. request letter No. NIL, dated: 24.12.2024 vide which request to removal of tree for clearing the land for construction.

It is therefore requested to do needful for felling of tree in both sides North & South portion at the earliest so that Solar developer start the work.

Encl: As above.

Signed by

Shyam Narayan Prajapati

Date: 26-12-2024 13:31:17

(S.N. Prajapati)
Executive Engineer (Solar)

Cc:

1. M/s Shimato Enterprises Private Ltd. with request to co-ordinate the Civil Officials, UJVNL Dhalipur for early action.
2. Assistant Engineer (Solar), UJVNL for necessary action.

evolve

-Energy Group-

CHENNAI - DELHI - MUMBAI - AHMEDABAD
COIMBATORE - SRILANKA - HONG KONG

Reg. Office:
No. 371, SIDCO Industrial Estate,
(NP) Ambattur, Chennai - 600098

www.evolveindia.in

info@evolveindia.in

044- 42105540

No: SEPL/TRPR/UJVNL/2.5/LR-05

27.12.2024

To

The Executive Engineer (Solar),
UJVN Limited,
"UJJWAL" GMS Road, Maharani Bagh,
Dehradun-248006.

Respected Sir,


**Sub: Requesting for Demolition of Encroached Houses in Site of 2.5 MW Canal Bank
Grid Connected Solar PV Plants.**

With reference to the LOI No: B-51/UJVNL/EE (Solar) / Dated:17.02.2024 & subsequent PPA signed on 7th of August 2024 for Setting-up of 2.5 MW Canal Bank Grid Connected Solar PV Plants on Yamuna Power Channel Near Bridge No-1, Dakpathar District- Dehradun, Uttarakhand.

We may be placed before your good office to request Ms. UJVNL to demolition of encroached houses in the site at the earliest for the smooth installation of the Solar Project which will facilitate us to proceed further to start the execution of work. This area covers more than 8000 sq. mts. Also, we have Attached the kml file for your review and reference through Mail.

We sincerely look forward to your positive response and swift action on this matter.

Thanks & Regards,



8

SHIMATO ENTERPRISES PRIVATE LIMITED

AN ISO 9001:2015, 14001:2015, & OHSAS 18001:2007 CERTIFIED COMPANY, NSIC & SSI / MSME Registered Company

GSTIN: 33AAPCS2173_1ZZ

evolve

CHENNAI DELHI KOLKATA AHMEDABAD
COIMBATORE GURILANKA HONG KONG

Reg. Office
No. 271, 3rd Floor, Industrial Estate,
100/1, Andulatai Chennai - 600090
www.evolveindia.in
Info@evolveindia.in
044 4210 5540

Ref No: SEPL/TRPR/UJVNL/2.5MW/TR-08

07-03-2025

To,
The Executive Engineer (Solar),
UJVNL Limited,
"Ujjwal", Maharani Bagh,
GMS Road, Dehradun-248006.

Subject: Request for Tree Cutting & Clearance – 2.5 MW Canal Bank Solar PV Project, Dakpathar, Dehradun

Respected Sir,

With reference to LOI No: B-51/UJVNL/EE (Solar) dated 17.02.2024 and the subsequent Power Purchase Agreement (PPA) signed on 7th August 2024 for the 2.5 MW Canal Bank Grid-Connected Solar PV Plant on Yamuna Power Channel near Bridge No-1, Dakpathar, District Dehradun, Uttarakhand.


We kindly seek your urgent support in cutting and clearing the trees on both sides of the canal bank. A total of 318 trees are present at the site, which need to be cleared to enable the commencement of project construction activities. We have enclosed the detailed tree list for your reference.

We seek your immediate attention to this matter, as it will help us proceed with the planned schedule.

Thank you for your time and consideration. We look forward to your positive response.

For Shimato Enterprises Private Limited,

EE (CIVIL), UJVNL, Dhalipur



Authorized Signatory

Enclosed: Detailed Tree List

Please after joint inspection, above mentioned trees are required to removed on urgent basis and as early as possible. It is therefore take necessary action on urgent basis.

For E.E. (Solar)
UJVNL Limited
GMS Road
Dehradun-248006

SHIMATO ENTERPRISES PRIVATE LIMITED

AN ISO 9001:2015 14001:2015 & OHSAS 18001:2007 CERTIFIED COMPANY. NSIC & ISI / MSME Registered Company

GSTIN: 33AAPCS2173L1ZZ

CC/13 Shimato Enterprises Pvt Ltd for UJVNL Limited
necessary action

② NE (Solar) for m.d.

No. 50/UJVNL/EE (Solar) | Date: 10/03/2025

Ref No: SEPL/TRPR/UJVNL/2.5MW/TR-12

19-03-2025

To,
The Executive Engineer (Solar),
UJVNL Limited,
"Ujjwal", Maharani Bagh,
GMS Road, Dehradun-248006.

Subject: Urgent Request for Intervention – 2.5 MW Canal Bank Solar PV Plant Installation

Respected Sir,

With reference to LOI No: B-51/UJVNL/EE(Solar), dated 17.02.2024, and the subsequent Power Purchase Agreement (PPA) signed on 07.08.2024, for the development of a 2.5 MW Canal Bank Grid-Connected Solar PV Plant on the Yamuna Power Channel near Bridge No-01, Dakpathar, District-Dehradun, Uttarakhand, we request your immediate intervention.


The SDM office has stopped our work at the site and is threatening to impose substantial fines on our machineries deployed at site. Despite presenting the letter issued by UJVNL, the SDM office has outrightly rejected it, insisting that all necessary approvals and clearances must be obtained by UJVNL through appropriate channels of communication with the respective government departments.

Further we request you to kindly provide necessary clearance for leveling of land and cleaning unwanted soil by shifting from south side to north side within the UJVNL boundary. Meantime, we request you to kindly take necessary steps for removal of trees on the South side of the canal. Hence our fencing and piling work will start.

The ongoing delays due to these unforeseen restrictions are significantly impacting our project timelines. Therefore, we urge UJVNL to take the necessary steps to secure the requisite permissions at the earliest to ensure uninterrupted progress at the site.

We sincerely appreciate your time and prompt attention to this matter and look forward to your positive response at the earliest.

For Shimato Enterprises Private Limited,



Authorized Signatory

SHIMATO ENTERPRISES PRIVATE LIMITED

AN ISO 9001:2015 14001:2015, & OHSAS 18001:2007 CERTIFIED COMPANY, NSIC & SSI - MSME Registered Company

GSTIN: 33AAPCS2173L1ZZ

Ref No: SEPL/TRPR/UJVNL/2.5MW/TR-15

03-04-2025

To,
The Executive Engineer (Solar),
UJVN Limited,
"Ujjwal", Maharani Bagh,
GMS Road, Dehradun-248006.

Subject: Request Urgent support – 2.5 MW Canal Bank Solar PV Plant Installation

Respected Sir,

With reference to LOI No. B-51/UJVNL/EE(Solar), dated 17.02.2024, and the subsequent Power Purchase Agreement (PPA) signed on 07.08.2024 for the development of a 2.5 MW Canal Bank Grid-Connected Solar PV Plant on the Yamuna Power Channel near Bridge No-01, Dakpathar, District Dehradun, Uttarakhand, we would like to bring the following to your urgent attention.

We have been carrying out land leveling work on the north side of the canal. However, this work has been obstructed by encroaching residents within the proposed solar project area. This situation has not only delayed project execution but has also raised serious safety concerns for our personnel.

We urgently seek your intervention to resolve this issue and ensure the safety of our team. Furthermore, we kindly request you to coordinate with the local government administration and arrange for police support to clear the encroachment at the earliest, allowing the work to resume without further disruptions.

Your prompt support in this matter is crucial to ensuring the smooth progress of the project.

Thank you for your immediate attention and cooperation.

For Evolve Green Energies Private Limited,



Authorized Signatory

EVOLVE GREEN ENERGIES PRIVATE LIMITED (formally known as M/s. SHIMATO ENTERPRISES PRIVATE LIMITED)

AN ISO 9001 :2015, 14001 :2015 & OHSAS 18001 :2007 CERTIFIED COMPANY, NSIC & SSI / MSME Registered Company

GSTIN: 33AAPCS217311ZZ | CIN: U74990TN2011PTC078851



Project execution has been significantly delayed due to the following reasons:

- Some residents on the north side of the canal have not yet vacated their premises. We have informed them, and they have stated that they will vacate only after the Eid festival.
- Tree cutting and relocation of existing poles and transformers at the designated site by UJVNL.
- Intervention by the DM office, Dakpathar, which has stopped land leveling work (a request letter was submitted to UJVNL in this work stopped at site and for resolution on 19.03.2025).

As the land leveling and fencing work are dependent on tree clearance and soil shifting, we urgently request UJVNL to obtain necessary clearance from DM office for leveling of land and cleaning unwanted soil by shifting from south side to north side within the UJVNL boundary. Meantime, we request you to kindly take necessary steps for removal of trees on the South side of the canal and Support to relocate the existing electrical poles and transformers from the designated solar installation area.

Also, we request you to provide an expected completion date for tree clearance, as our project execution schedule & material delivery is directly dependent on this activity.

Our primary focus has been on land leveling and fencing work. Once the fencing work is completed, we will promptly deliver the materials to the site. The installation will be carried out in one continuous stretch, ensuring a smooth and efficient process without any interruptions.

For further coordination, our Liaisoning representative, Mr. Anjan Chatterjee, remains in regular contact with UJVNL.

We sincerely appreciate your support and request your prompt confirmation on the above matters at the earliest. Thank you for your cooperation.

Sincerely,

For Evolve Green Energies Private Limited,



Authorized Signatory

- Enclosed: 1) Work Progress Photo.
2) Project Progress Report. .
3) SDM Office Instruction document.

Ref No: SEPL/TRPR/UJVNL/2.5MW/TR-16

03-04-2025

To,
The Executive Engineer (Solar),
UJVNL Limited,
"Ujjwal", Maharani Bagh,
GMS Road, Dehradun-248006.

Subject: Request for Tree Cutting & Clearance – 2.5 MW Canal Bank Solar PV Project, Dakpathar, Dehradun

Respected Sir,

Ref:

1. Our Request Letter Ref. No. Nil, dated: 24-12-2024
2. Your Letter Ref. No: Nil, dated: 26-12-2024
3. Our Request Letter Ref No. SEPL/TRPR/UJVNL/2.5MW/TR-08, dated: 07-03-2025
4. Our Request Letter Ref No: SEPL/TRPR/UJVNL/2.5MW/TR-12, dated: 19-03-2025
5. Our Request Letter Ref No: SEPL/TRPR/UJVNL/2.5MW/TR-13, dated: 25-03-2025

With reference to LOI No. B-51/UJVNL/EE(Solar), dated 17.02.2024, and the subsequent Power Purchase Agreement (PPA) signed on 07.08.2024 for the development of a 2.5 MW Canal Bank Grid-Connected Solar PV Plant on the Yamuna Power Channel near Bridge No-01, Dakpathar, District Dehradun, Uttarakhand, we would like to bring the following to your kind attention.

We have been carrying out land leveling work on the north side of the canal. To ensure smooth project execution, we need to begin work on the south side as well. Therefore, we kindly request you to expedite the clearance of trees to facilitate the timely commencement of construction activities on the south side of the canal.

We have submitted multiple requests regarding this matter, as referenced in our previous letters (Ref. No. 1, 3, 4, and 5). Furthermore, as per Ref. No. 2, your letter has been forwarded to the Executive Engineer (Civil), Dhalipur, for tree clearance work. Additionally, as per Ref. No. 3, we have already provided the tree list to your office for necessary action.



CHENNAI - DELHI - MUMBAI - AHMEDABAD
KOLKATTA - COIMBATORE - MADURAI

Reg. Office:
No.371, SIDCO Industrial Estate,
(NP) Ambattur, Chennai - 600098.

www.evolveindia.in

info@evolveindia.in

044- 4210 5540



We seek your immediate attention to this matter, as the timely clearance of trees is crucial for maintaining our project schedule.

Thank you for your time and consideration. We look forward to your positive response at the earliest.

For Evolve Green Energies Private Limited,

Authorized Signatory

EVOLVE GREEN ENERGIES PRIVATE LIMITED (formally known as M/s. SHIMATO ENTERPRISES PRIVATE LIMITED)

AN ISO 9001 :2015, 14001 :2015 & OHSAS 18001 :2007 CERTIFIED COMPANY, NSIC & SSI / MSME Registered Company

GSTIN: 33AAPCS2173L1ZZ | CIN: U74990TN2011PTC078851

No. 82 ALJVN/EE (Solar)/

Date: 05-04-2025

Subject: Request for Tree cutting & Clearance- 2.5 MW Canal Bank Solar PV Project, Dakpathar, Dehradun.

Executive Engineer (Civil)
UJVN Ltd.
Dhalipur, Dehradun.

Please find enclosed herewith the letter No. SEPL/TRPR/UJVNL/2.5 MW/TR-16,
Dated: 03.04.2025 of M/s Evolve Green Energy Pvt.Ltd. Chennai, requesting for tree
clearance.

In this regard, please do needful for removal of tree under site of 2.5 MW Canal Bank Solar PV Plant near bridge no-1 Dakpathar on Urgent Basis so that Plant can be installed in time.

Encl: As Above

(S. N. Prajapati)
Executive Engineer (Solar)

Cc: M/s Evolve Green Energies Private Limited, Chennai with request to co-ordinate with Civil Officials for early action.



यूजेवीएन लिमिटेड

UJVNL LIMITED

(A Govt. of Uttar Pradesh Enterprise)

उत्तर प्रदेश विद्युत निगम (संयुक्त) लिमिटेड, यमना कालोनी, यमना रोड, देहरादून-248006 (Uttarakhand), Phone: 0135-2764100 Fax: 0135-2764101
Office of the Executive Engineer (Solar), "Ujjwal", Maharani Bagh, G.M.S. Road, Dehradun-248006 (Uttarakhand), Phone: 0135-2764100 Fax: 0135-2764101
CIN No 401011R2001SGC025866

ISO 9001:2015, ISO 14001:2015 & 45001:2017 Certified

पत्रांक: ४५ / यूजेवीएन लि०/अधि.अभि.(सोलर)/

दिनांक: ०५-०४-२०२५

विषय- डाकपत्थर शक्तिनहर के पुल नं०-०१ के समीप लग रहे २.५ मे०वा० सौर संयंत्र में पुलिसा सुरक्षा उपलब्ध कराये जाने के सम्बन्ध में।


उपजिलाधिकारी
विकास नगर, देहरादून।

महोदय कृपया उपरोक्त विषयक अवगत कराना है कि उत्तराखण्ड सरकार की महत्वाकांक्षी २.५ मे०वा० सौर संयंत्र परियोजना की स्थापना हेतु यूजेवीएन लि० के माध्यम से मै० इवात्व ग्रीन एनर्जी प्रा० लि० सौर विकासकर्ता द्वारा संपादित किया जा रहा है। वर्तमान में भूमि के समतलीकरण का कार्य किया जा रहा है। प्रस्तावित सौर भूमि पर वहां पर स्थित अतिक्रमण व्यक्तियों द्वारा बार-बार कार्य में व्यवधान उत्पन्न किया जा रहा है। जिसके कारण उक्त सौर संयंत्र लगाने में विलम्ब हो रहा है।

सौर विकासकर्ता द्वारा कार्य कर रहे कर्मचारियों की सुरक्षा किये जाने एवं बार-बार कार्य में व्यवधान उत्पन्न न हो, के लिए सौर विकासकर्ता द्वारा पुलिस बल की मांग की गयी है। (प्रतिलिपि संलग्न)।

अतः उक्त के सम्बन्ध में आपसे निवेदन है कि उक्त २.५ मे०वा० सौर संयंत्र परियोजना को ससमय सम्पन्न कराये जाने के क्रम में, भूमि समतलीकरण कार्य किये जाने के दौरान डाकपत्थर शक्तिनहर के पुल-०१ के समीप पुलिस बल की व्यवस्था करवाये जाने का कष्ट करें।

संलग्नक: यथोपरि।


(एस.एन प्रजापति)

अधिशाली अभियन्ता (सोलर)

प्रतिलिपि:-

१. उपमहाप्रबन्धक(सोलर,एम०एम०एण्ड सी०एम०), यूजेवीएन लि०, गंगा भवन, यमना कालोनी, देहरादून।
२. अधिशाली अभियन्ता (जानपद), यूजेवीएन लि०, ढालीपुर, देहरादून को सूचनार्थ एवं आवश्यक कार्यवाही हेतु प्रेषित।
३. मै० इवात्व ग्रीन एनर्जी प्रा० लि० को इस आशय से प्रेषित कि कृपया उपजिलाधिकारी कार्यालय से समन्वय स्थापित कर कार्य को अतिशीघ्र पूर्ण करने का कष्ट करें।

Ref No: SEPL/TRPR/UJVNL/2.5MW/TR-17

17-04-2025

To,
The Executive Engineer (Solar),
UJVNL Limited,
"Ujjwal", Maharani Bagh,
GMS Road, Dehradun-248006.

**Subject: Request for Removal of Encroachment and Tree Cutting Clearance – 2.5 MW Canal Bank
Solar PV Project, Dakpathar, Dehradun**

Ref:

1. Our Request Letter Ref. No. Nil, dated 24.12.2024
2. Your Letter Ref. No. Nil, dated 26.12.2024
3. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-08, dated 07.03.2025
4. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-12, dated 19.03.2025
5. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-13, dated 25.03.2025
6. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-15, dated 03.04.2025
7. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-16, dated 03.04.2025
8. Your Letter Ref. No. 82/UJVNL/EE(Solar), dated 05.04.2025
9. Your Letter Ref. No. 84/UJVNL/Superintendent (Solar), dated 05.04.2025

With reference to LOI No. B-51/UJVNL/EE(Solar), dated 17.02.2024, and the subsequent Power Purchase Agreement (PPA) signed on 07.08.2024 for the development of a 2.5 MW Canal Bank Grid-Connected Solar PV Plant on the Yamuna Power Channel near Bridge No. 01, Dakpathar, District Dehradun, Uttarakhand.

We would like to inform you that the construction of the retaining wall and land leveling work on the north side of the canal bank solar site is expected to be completed within the next couple of days, excluding the areas affected by encroachments and existing trees. However, the installation of fencing has been delayed due to the continued presence of certain residents who have not yet vacated the proposed solar installation area allotted by UJVNL.

We kindly request your esteemed office to take prompt and necessary action for the removal of encroachments and to expedite the tree cutting clearance, to ensure the project continues without interruption.

EVOLVE GREEN ENERGIES PRIVATE LIMITED (formally known as M/s. SHIMATO ENTERPRISES PRIVATE LIMITED)

AN ISO 9001:2015, 14001:2015 & OHSAS 18001:2007 CERTIFIED COMPANY, NSIC & SSII / MSME Registered Company

GSTIN: 33AAPCS2173L1ZZ | CIN: U74990TN2011PTC078851

For your reference, please find the attached files below.

1. Hand-sketch layout marking the encroachment-affected area.
2. Work Progress Photos.
3. Solar Plant Layout Drawing


Your prompt support in this matter is crucial to ensuring the smooth progress of the project.

For Evolve Green Energies Private Limited,



Authorized Signatory

Encroachment Area Marking Hand Sketch:

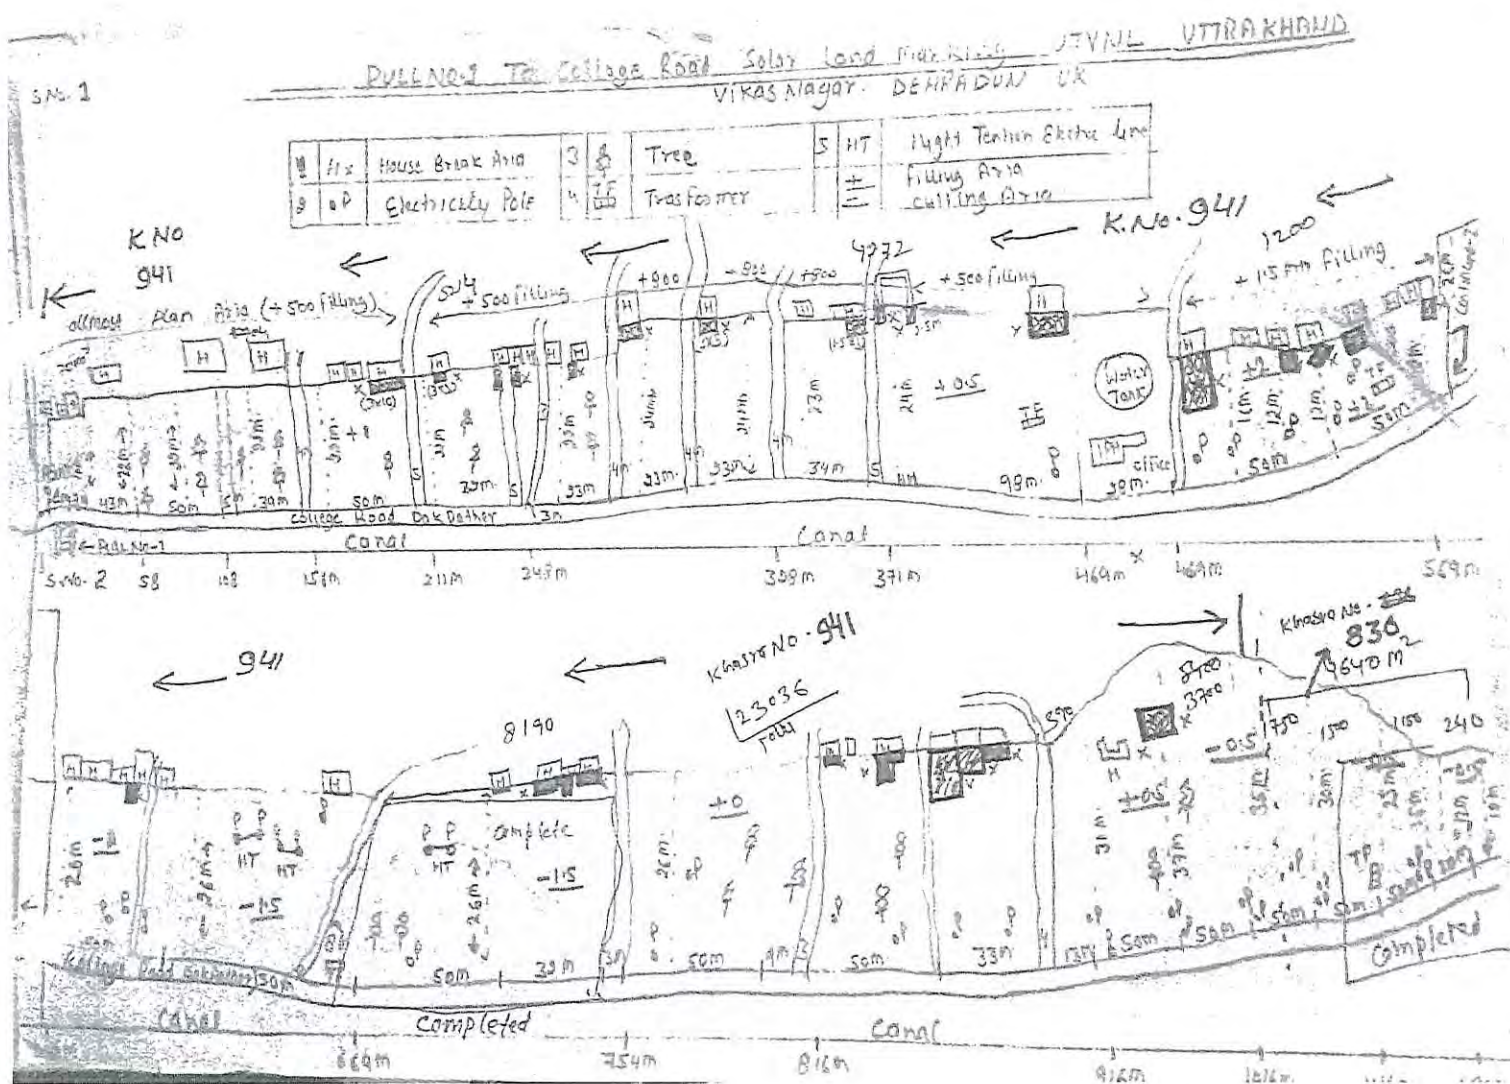

Ref No: SEPL/TRPR/UJVNL/2.5MW/TR-18

23-04-2025

To,
The Executive Engineer (Solar),
UJVNL Limited,
"Ujjwal", Maharani Bagh,
GMS Road, Dehradun-248006.

Subject: Project Progress & Request for Time Extension – 2.5 MW Canal Bank Solar PV Project, Dakpathar, Dehradun

Respected Sir,

Ref:

1. Our Request Letter Ref. No. Nil (Tree Cutting Work), dated 24.12.2024
2. Our Request Letter Ref. No. Nil (Existing Transmission line & Transformer Shifting), dated 24.12.2024
3. Your Letter Ref. No. Nil, dated 26.12.2024
4. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/LR-05, dated 27.12.2024
5. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-08, dated 07.03.2025
6. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-12, dated 19.03.2025
7. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-13, dated 25.03.2025
8. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-15, dated 03.04.2025
9. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-16, dated 03.04.2025
10. Your Letter Ref. No. 82/UJVNL/EE(Solar), dated 05.04.2025
11. Your Letter Ref. No. 84/UJVNL/Superintendent (Solar), dated 05.04.2025
12. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-17, dated 17.04.2025

With reference to LOI No. B-51/UJVNL/EE(Solar), dated 17.02.2024, and the Power Purchase Agreement (PPA) signed on 07.08.2024 for the development of the 2.5 MW Canal Bank Grid-Connected Solar PV Plant on the Yamuna Power Channel near Bridge No. 01, Dakpathar, District Dehradun, we would like to share the current project status and seek your support regarding certain pending issues.

Project Progress

We are pleased to inform you of the following project developments (Work Progress Photos Attached) for your kind perusal.

- The construction of the retaining wall on the north side of the canal bank is nearing completion.
- Land leveling is in progress, and fencing work has commenced on the north side.
- Land leveling on the south side has been completed, except in areas with existing trees to be removed.

EVOLVE GREEN ENERGIES PRIVATE LIMITED (formerly known as M/s. SHIMATO ENTERPRISES PRIVATE LIMITED)

AN ISO 9001:2015, 14001:2015 & OHSAS 18001:2007 CERTIFIED COMPANY, NSIC & SSI / MSME Registered Company

GSTIN: 33AAPCS2173L1ZZ | CIN: U74990TN2011PTC078851



Challenges and Pending Issues

Despite the above progress, the project is currently facing delays due to:

- Tree-cutting and removal at site (It was informed Tender will be floated for removal of trees)
- Encroachment issues (It is informed that notice will be served to encroached dwellers to remove the encroachments -Yet to receive any official confirmation)
- Shifting of existing 11kV electrical poles, transmission line, and transformer.

We have already submitted requests to M/s. UJVNL on these issues, as detailed below:

- Tree-Cutting & Removal: Refer to Letters 1, 5, 6, 7, 9, and 12
- Encroachment Clearance: Refer to Letters 4, 7, 8, 11, and 12
- Shifting of Existing Electrical Poles, Transformers: Refer to Letters 2 and 7

We kindly request your esteemed office to take prompt and necessary action for the removal of encroachments and to expedite the tree cutting clearance, to ensure the project continues without interruption.

Request for Time Extension

Considering the above unforeseen challenges beyond our control, we hereby request a three (3) month extension to the project completion timeline, without levy of any penalties.

We sincerely hope for your understanding and support to help maintain the overall project momentum and meet the intended objectives.

Thank you for your continued cooperation.

For Evolve Green Energies Private Limited,

Authorized Signatory

Enclosed: 1. Reference Letters.
2. Work Progress Photos.

EVOLVE GREEN ENERGIES PRIVATE LIMITED (formally known as M/s. SHIMATO ENTERPRISES PRIVATE LIMITED)

AN ISO 9001 :2015, 14001 :2015 & OHSAS 18001 :2007 CERTIFIED COMPANY. NSIC & SSI / MSME Registered Company

GSTIN: 33AAPCS2173L1ZZ | CIN: U74990TN2011PTC078851

Ref No: SEPL/TRPR/UJVNL/2.5MW/TR-19

02-05-2025

To,
The Executive Engineer (Solar),
UJVNL Limited,
"Ujjwal", Maharani Bagh,
GMS Road, Dehradun-248006.

Subject: Request for Extension of Project Completion Timeline - 2.5 MW Canal Bank Solar PV Project, Dakpathar, Dehradun

Respected Sir,

Ref:

1. Our Request Letter Ref. No. Nil (Tree Cutting Work), dated 24.12.2024
2. Our Request Letter Ref. No. Nil (Existing Transmission line & Transformer Shifting), dated 24.12.2024
3. Your Letter Ref. No. Nil, dated 26.12.2024
4. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/LR-05, dated 27.12.2024
5. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-08, dated 07.03.2025
6. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-12, dated 19.03.2025
7. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-13, dated 25.03.2025
8. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-15, dated 03.04.2025
9. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-16, dated 03.04.2025
10. Your Letter Ref. No. 82/UJVNL/EE(Solar), dated 05.04.2025
11. Your Letter Ref. No. 84/UJVNL/Superintendent (Solar), dated 05.04.2025
12. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-17, dated 17.04.2025
13. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-18, dated 23.04.2025
14. Your Letter Ref. No. 97/UJVNL/EE(Solar), dated 24.04.2025

With reference to LOI No. B-51/UJVNL/EE(Solar) dated 17.02.2024, and the Power Purchase Agreement (PPA) signed on 07.08.2024 for the development of the 2.5 MW Canal Bank Grid-Connected Solar PV Plant on the Yamuna Power Channel near Bridge No. 01, Dakpathar, District Dehradun

We would like to sincerely thank you for floating the short-term tender for tree cutting work through M/s. UJVNL on 24.04.2025. We are hopeful that the tree cutting work will be completed this month.

Further, as per the guidance received, we have engaged with the concerned local administrative authorities — including the Tehsildar, Patwari, and Executive Engineer (Civil), Dhalipur — regarding encroachment clearance. However, the timeline for complete resolution of the encroachment issue remains uncertain at this stage.



CHENNAI - DELHI - MUMBAI - AHMEDABAD
KOLKATTA - COIMBATORE - MADURAI

Reg. Office:
No.371, SIDCO Industrial Estate,
(NP) Ambattur, Chennai - 600098.

www.evolveindia.in

info@evolveindia.in

044- 4210 5540



In view of these unforeseen challenges, we hereby request an extension of four (4) months to the project completion timeline, effective from the date of completion of all required clearances (including encroachment clearance and tree cutting), without the levy of any penalties.

We remain deeply grateful for your continued cooperation and support and look forward to your kind consideration of our request.

For Evolve Green Energies Private Limited,

Authorized Signatory

EVOLVE GREEN ENERGIES PRIVATE LIMITED (formally known as M/s. SHIMATO ENTERPRISES PRIVATE LIMITED)

AN ISO 9001 :2015, 14001 :2015 & OHSAS 18001 :2007 CERTIFIED COMPANY, NSIC & SSI / MSME Registered Company

GSTIN: 33AAPCS2173L1ZZ | CIN: U74990TN2011PTC078851

Ref No: SEPL/TRPR/UJVNL/2.5MW/TR-20

17-05-2025

To,
The Executive Engineer (Solar),
UJVNL Limited,
"Ujjwal", Maharani Bagh,
GMS Road, Dehradun-248006.

Subject: Request for Extension of Project Completion Timeline - 2.5 MW Canal Bank Solar PV Project, Dakpathar, Dehradun

Respected Sir,

Ref:

1. Our Request Letter Ref. No. Nil (Tree Cutting Work), dated 24.12.2024
2. Our Request Letter Ref. No. Nil (Existing Transmission line & Transformer Shifting), dated 24.12.2024
3. Your Letter Ref. No. Nil, dated 26.12.2024
4. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/LR-05, dated 27.12.2024
5. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-08, dated 07.03.2025
6. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-12, dated 19.03.2025
7. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-13, dated 25.03.2025
8. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-15, dated 03.04.2025
9. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-16, dated 03.04.2025
10. Your Letter Ref. No. 82/UJVNL/EE(Solar), dated 05.04.2025
11. Your Letter Ref. No. 84/UJVNL/Superintendent (Solar), dated 05.04.2025
12. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-17, dated 17.04.2025
13. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-18, dated 23.04.2025
14. Your Letter Ref. No. 97/UJVNL/EE(Solar), dated 24.04.2025
15. Our Request Letter Ref. No. SEPL/TRPR/UJVNL/2.5MW/TR-19, dated 02.05.2025

We are writing to provide an update on the progress of the 2.5 MW Canal Bank Grid-Connected Solar PV Plant project on the Yamuna Power Channel near Bridge No. 01, Dakpathar, District Dehradun, as per the Letter of Intent (LOI) No. B-51/UJVNL/EE(Solar) dated 17.02.2024 and the Power Purchase Agreement (PPA) signed on 07.08.2024. We also seek your kind approval for a four-month extension to the project completion timeline due to unforeseen challenges beyond our control.

Work Progress Update:

1. Retaining wall construction has been successfully completed.
2. Fencing work is completed, except in areas affected by encroachments and existing trees.
3. Land leveling is completed, except in areas with encroachments and trees.

EVOLVE GREEN ENERGIES PRIVATE LIMITED (formally known as M/s. SHIMATO ENTERPRISES PRIVATE LIMITED)

AN ISO 9001:2015, 14001:2015 & OHSAS 18001:2007 CERTIFIED COMPANY. NSIC & SSI / MSME Registered Company

GSTIN: 33AAPCS217311ZZ | CIN: U74990TN2011PTC078851



Reasons for Delay: Despite our diligent efforts, the project has faced significant delays due to the following issues:

1. **Encroachment Issues:** Residents have not vacated the proposed solar installation area allocated by M/s. UJVNL, hindering site preparation and layout finalization.
2. **Tree Cutting Delays:** Although M/s. UJVNL floated a tender for tree cutting, the work has not yet commenced, further delaying site clearance.

We have also submitted the Land Memorandum of Understanding (MoU) documents to M/s. UJVNL; however, the documents have not yet been signed by M/s. UJVNL. Additionally, the demarcation process was completed only on 14th May 2025 by Government officials, which has further impacted on the project timeline.

As manufacturers of solar modules and inverters, we have been unable to proceed with material supply to the site due to unresolved issues related to land allocation and tree removal.

We have submitted multiple requests to M/s. UJVNL for land allocation free of encroachment and the removal of trees at proposed site, but these remain pending.

Request for Extension: In view of these unforeseen circumstances, we respectfully request a four (4) month extension to the project completion timeline, effective from the date of completion of all required clearances, including encroachment clearance and tree cutting. We further request that no penalties be levied, as the delays are attributable to factors beyond our control. This extension will enable us to deliver a high-quality project that aligns with the tender's technical standards.

We deeply appreciate your continued support and cooperation and kindly urge your favorable consideration of this request.

Thank you for your understanding and support. We look forward to your positive response.

For Evolve Green Energies Private Limited,

Authorized Signatory

Ref No: SEPL/TRPR/UJVNL/2.5MW/TR-24

29-05-2025

To,
The Executive Engineer (Solar),
UJVN Limited,
"Ujjwal", Maharani Bagh,
GMS Road, Dehradun-248006.

Subject: Material Procurement Details – 2.5 MW Canal Bank Grid-Connected Solar PV Plant

Respected Sir,

With reference to LOI No. B-51/UJVNL/EE(Solar) dated 17.02.2024 and the Power Purchase Agreement (PPA) signed on 07.08.2024 for the 2.5 MW Canal Bank Grid-Connected Solar PV Plant on the Yamuna Power Channel near Bridge No-01, Dakpathar, District Dehradun, Uttarakhand, we are writing to inform you of the following:

We have procured the required Solar Modules and Inverters for the project. As a precautionary safety measure, these materials are currently stored at our Chennai Warehouse. Once the site clearance process is completed, we will deliver the materials to the project site.

For your kind reference, please find attached the following documents:

- Solar Module Proforma Invoice
- Inverter Order Acknowledgement Note (OAN)



Note:

- Required Solar Modules for the Project: 585 Wp – 5,824 nos.
- Required On-Grid Inverters for the Project: 350 kW – 7 nos.

For Evolve Green Energies Private Limited,



Authorized Signatory

SHIMATO ENTERPRISES PRIVATE LIMITED Regd. Office : #371, SIDCO Industrial Estate, North Phase, Ambattur, Chennai-600098 CIN NO.: U74990TN2011PTC078851					
PROJECT ID: TND-012		ORDER ACKNOWLEDGEMENT NOTE			
OAN NO. : TND-SEPL-001 / 2024-25		DATE :03-01-2025	LOA No: B-51/UJVNL/EE (Solar)	LOA DATE :	17-02-2024
Ordering Customer			Billing customer		
Name	SHIMATO ENTERPRISES PRIVATE LIMITED		Name	SHIMATO ENTERPRISES PRIVATE LIMITED	
Address	No.371, SIDCO Industrial Estate, North Phase, Ambattur		Address	No.371, SIDCO Industrial Estate, North Phase, Ambattur	
City	Chennai-600098		City	Chennai-600098	
State	TAMIL NADU		State	TAMIL NADU	
GST No	33AAPCS2173L1ZZ		GST No	33AAPCS2173L1ZZ	
Contact Person	Mr. PRASAD.S.K		Contact Person	Mr. PRASAD.S.K	
Phone No	99400 19713		Phone No.	99400 19713	
Account Holder Name : Mr. PRASAD.S.K			Phone :+91 99400 19713		
Delivery Customer			Paying Authority		
Name	Shimato Enterprises Private Limited C/o. 2.5MW UJVNL Solar Project		Name	SHIMATO ENTERPRISES PRIVATE LIMITED	
Address	Yamuna Power Channel Near Bridge No-1 Dakpathar District,		Address	No.371, SIDCO Industrial Estate, North Phase, Ambattur	
City	Dehradun -248125		City	Chennai-600098	
State	Uttarakhand		State	TAMIL NADU	
GST No			GST No	33AAPCS2173L1ZZ	
Contact Person			Contact Person	Mr. PRASAD.S.K	
Phone No			Phone No	99400 19713	
SHIMATO ENTERPRISES PRIVATE LIMITED thanksfully acknowledges your order for the under mentioned items in accordance with the terms and conditions cited hereunder and agreed upon in the process earlier & conveyed in writing or otherwise by any authorized official of the company or its reseller / associates.					
Sl. No.	Item Description	Qty (No)	Rate (Rs.)	Total Amount (Rs.)	
1	EVVO 350 KW On Grid Inverter	7			
RUPEES:			GST @ 12%		
			GRAND TOTAL		
			ROUNDED OFF TO		
Payment Terms : Built, Own, Operate & Transfer (BOOT) Model					
Warranty :Inverter - 8 years As per Manufacturer recommendation					
PROJECT COMPLETION : 18th JUNE 2025			MATERIAL DELIVERY DATE:		
Requisitions to customer related to Purchase Order			Freight & Insurance : INCLUDED		
(The Order is processed for execution subject to the above)					
Distribution with Order Copy			For SHIMATO ENTERPRISES PRIVATE LIMITED		
1. Order Customer			 AUTHORIZED SIGNATORY		
2. Mfg. Unit (Original P.O & Order Analysis)					
3. File Copy					
GST No:33AAPCS2173L1ZZ					

AATMANIRBHAR SOLAR PRIVATE LIMITED

304, Vraj Valencia, Sola

Overbridge, SG Highway,

Ahmedabad, Ahmedabad,

Gujarat, Ahmedabad City,

GUJARAT-380060

GSTIN : 24AATCA8654LIZY

PI NO : PI/23-24/264

PI Date : 06/12/2024

Transportation Terms: Ex-work

Payment Terms: 100% advance

BILL TO

SHIMATO ENTERPRISES PVT LTD

#371, SIDCO Industrial Estate, North Phase, Ambattur, Chennai-

600 098,

, India

GSTIN : 33AAPCS2173LIZZ

SHIP TO

SHIMATO ENTERPRISES PVT LTD

#371, SIDCO Industrial Estate, North Phase, Ambattur, Chennai-

600 098,

, India

GSTIN : 33AAPCS2173LIZZ

Sr No	Description of Goods	HSN Code	QTY	Rate	Discount	Taxable Amount	Tax%	Tax Amount	Total
1	AC253-1-ASPL-TP-Solar module, Topcon: 585 Wp half cut Glass to glass modules, Make: ASPL	85414300	25200.00 PCS	6.00	0.00	151200.00	12%	18144.00	169344.00
	Total				₹ 0.00	₹ 151200.00		₹ 18144.00	₹ 169344.00

Amount In Words: Eighteen Crores Thirty One Lakh Seventy Three Thousand Five Hundred Sixty Nine Only /-

HSN Code	Amount	CGST	SGST	Total Tax
85414300	151200.00	(6.00%) 9072.00	(6.00%) 9072.00	(12.00%) 18144.00
Grand Total	₹ 151200.00	₹ 9072.00	₹ 9072.00	₹ 18144.00

Currency: INR

Tax Amount In Words: Eighteen Thousand Six Hundred Sixty Nine Only

Terms & Conditions

Notes:

Bank Details:

Bank name: HDFC Bank


Account name: Aatmanirbhar Solar Pvt. Ltd.

Account no. : 50200070229116

Branch name: Ashram road Ahmedabad

Thank you for your Business

This is a computer-generated copy and does not require any signature.



Invoice To Shimato Enterprises Pvt Ltd #371, SIDCO Industrial Estate Opposite Godrej 2nd Gate North Phase, Ambattur Chennai-600098 Ph: 044 - 4210 5540/7550010795 GSTIN/UID: 33AAPCS2173L1ZZ State Name : Tamil Nadu, Code : 33 CIN: U74990TN2011PTC078851	Voucher No. WO-EPC-100004	Dated 3-Dec-24
Consignee (Ship to) Shimato Enterprises Pvt Ltd #371, SIDCO Industrial Estate Opposite Godrej 2nd Gate North Phase, Ambattur Chennai-600098 Ph: 044 - 4210 5540/7550010795 GSTIN/UID : 33AAPCS2173L1ZZ State Name : Tamil Nadu, Code : 33	Reference No. & Date.	Mode/Terms of Payment As Per Attached Annexure
	Dispatched through	Other References WO-EPC-100004
Supplier (Bill from) KADIAN INFRASTRUCTURE PVT LTD WZ-10B, ASALATPUR VILLAGE, A-2, Block , JANAKPURI , NEWDELHI-110058. GSTIN/UID : 07AAECK0465E2ZS State Name : Delhi, Code : 07	Terms of Delivery For UJVN - 3.5MWp Utterakhand	

Sl No.	Description of Services	Due on	Quantity	Rate	per	Disc. %	Amount
1	Installation and Commissioning Charges 3.5MWp @12/Watt Scope of Supply Ref to Annexure '1' Annexure '2' & Annexure '3' INPUT IGST @ 18%						4,20,00,000.00
					18 %		75,60,000.00
Total							₹ 4,95,60,000.00

Amount Chargeable (in words)

E. & O.E

INR Four Crore Ninety Five Lakh Sixty Thousand Only

Company's PAN : AAPCS2173L



for Shimato Enterprises Pvt Ltd

Prepared by

Verified by

Authorised Signatory

This is a Computer Generated Document

भारतीय गैर न्यायिक

एक सौ रुपये

Rs. 100

रु. 100

ONE
HUNDRED RUPEES



सत्यमेव जयते

भारत INDIA
INDIA NON JUDICIAL



28 MAY 2025

DF 774806

பா. தனிககவேல்

முத்தியூதான் கிராமசபையன்
உரிமம் எண். 5930/23/08-2
தாள். 19-12-08 எண். 20, திருவள்ளூர்
உ.அ.ப. கனகசபை, அம்பத்தூர், சென்னை-600098
774806 88894/89772 577

NO CLAIM CERTIFICATE

M/s. Evolve Green Energies Private Limited, a company incorporated under the laws of India, having its registered office at No.371, SIDCO Industrial Estate (NP), Ambattur, Chennai – 600098.

The M/s. Evolve Green Energies Private Limited was awarded the contract for the Setting up of a 2.5 MW(AC) Canal Bank Grid-Connected Solar PV Plant on the Yamuna Power Channel near Bridge No-1, Dakpathar, District - Dehradun, Uttarakhand, on a Build, Own, Operate & Transfer (BOOT) basis for UJVNL in the State of Uttarakhand, under LOA No. B-51/UJVNL/EE(Solar) dated 17-02-2024.

NOW, THEREFORE, M/s. Evolve Green Energies Private Limited hereby certifies and declares as follows:

1. We have no further claims or demands against the M/s.UJVNL arising out of or in connection with the said contract extension.



2. We shall not claim any compensation whatsoever due to the grant of this extension, nor claim any increase in the rates entered in our contract bond for the works carried out during the extended period.
3. We hereby confirm our acceptance of all the tender terms and conditions and those of the Power Purchase Agreement (PPA), as applicable.

This No Claim Certificate is issued solely for project timeline extension purpose only

For M/s. Evolve Green Energies Private Limited,



(Authorized Signatory)

Name: *Prasad. sika*

Designation: *Tendering Manager.*

Ref No: SEPL/TRPR/UJVNL/2.5MW/TR-25

03-06-2025

To,
The Executive Engineer (Solar),
UJVNL Limited,
"Ujjwal", Maharani Bagh,
GMS Road, Dehradun-248006.

Subject: Work Progress Update – 2.5 MW Canal Bank Solar PV Project, Dakpathar, Dehradun-Reg

Respected Sir,

With reference to LOI No. B-51/UJVNL/EE(Solar) dated 17.02.2024 and the Power Purchase Agreement (PPA) signed on 07.08.2024 for the 2.5 MW Canal Bank Grid-Connected Solar PV Plant located on the Yamuna Power Channel near Bridge No. 01, Dakpathar, District Dehradun, Uttarakhand.

We are pleased to inform you that the following works have been successfully completed at site:

1. **Retaining Wall Construction:** Completed along the north side of the canal bank to ensure the safety and stability of the plant.
2. **Land Leveling:** Completed in all accessible areas, excluding zones affected by existing encroachments and trees.
3. **Fencing Work:** Completed in all permissible areas, except in locations hindered by encroachments and Trees

Please find attached **Site Work Progress Photos (Annexure-I)** for your review.

However, unresolved site issues, including encroachments and tree-related obstructions, are currently impeding further progress. In view of these challenges, we kindly request an extension of the project timeline to ensure successful completion.

Thank you for your understanding and support.

For Evolve Green Energies Private Limited,




Authorized Signatory

Enclosed: Annexure-I: Site Work Progress Photo

Annexure-I (Work Progress Photos)

Site Name: 2.5 MW Canal Bank Solar PV Plant (UJVNL Project, Dakpathar, Uttarakhand)


Work Progress Report: 01-04-2025 to 15-04-2025

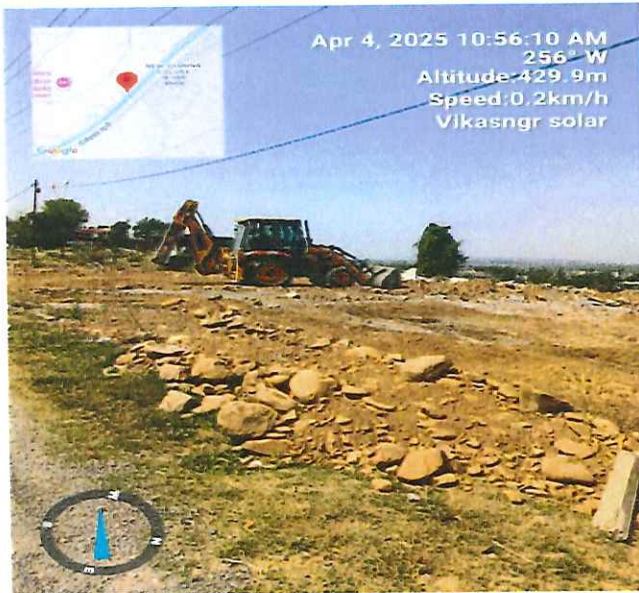

05-04-2025



05-04-2025

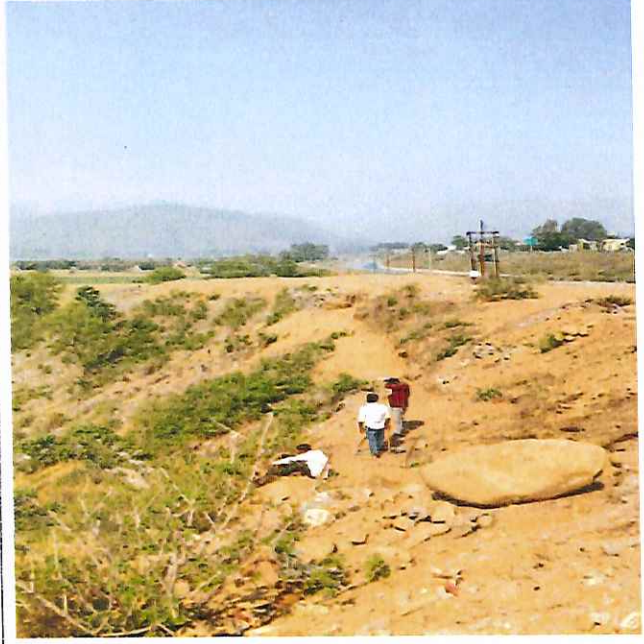

Annexure-I (Work Progress Photos)

Site Name: 2.5 MW Canal Bank Solar PV Plant (UJVNL Project, Dakpathar, Uttarakhand)

Work Progress Report: 01-04-2025 to 15-04-2025

07-04-2025



07-04-2025



07-04-2025







07-04-2025



Annexure-I (Work Progress Photos)

Site Name: 2.5 MW Canal Bank Solar PV Plant (UJVNL Project, Dakpathar, Uttarakhand)




Work Progress Report: 01-04-2025 to 15-04-2025

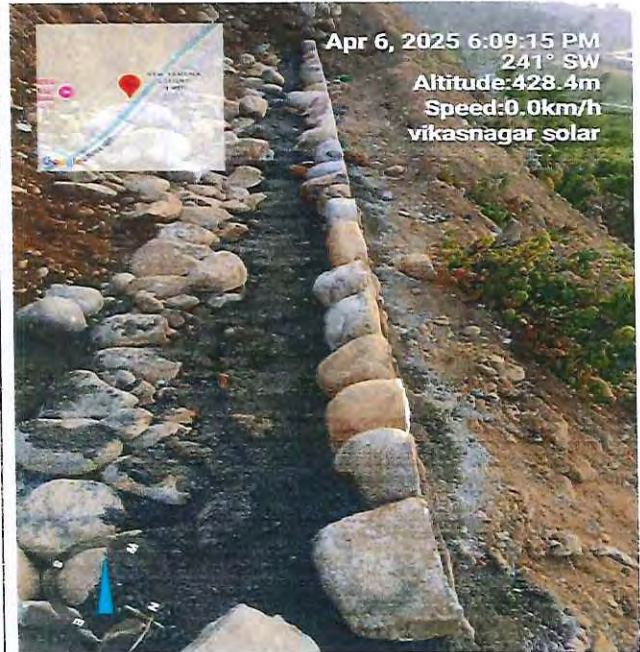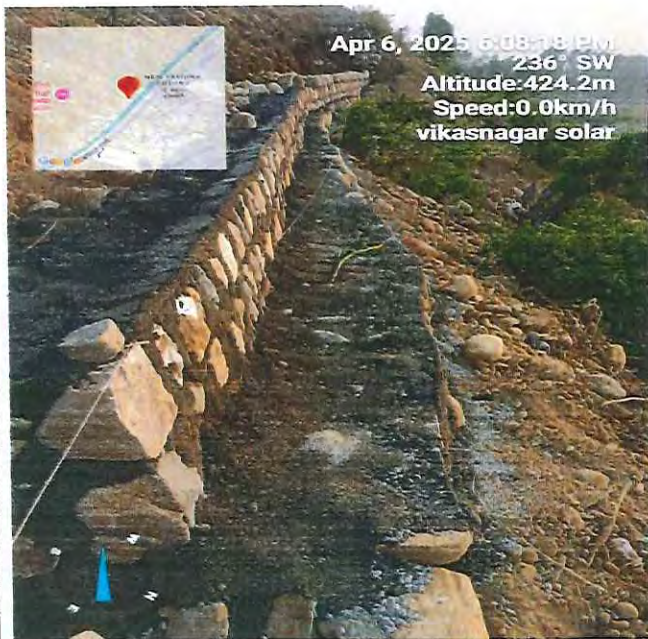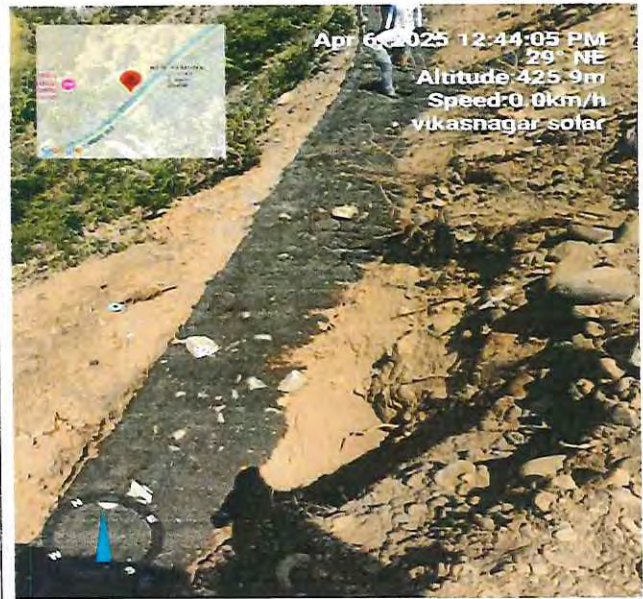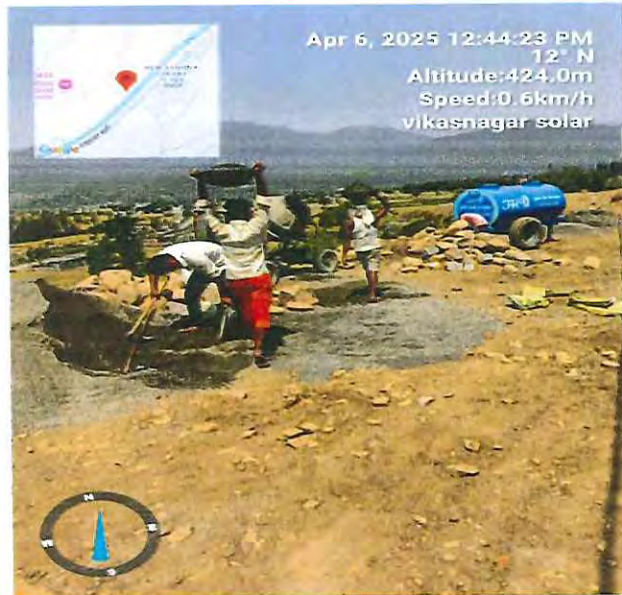

Annexure-I (Work Progress Photos)

Site Name: 2.5 MW Canal Bank Solar PV Plant (UJVNL Project, Dakpathar, Uttarakhand)

Work Progress Report: 16-04-2025 to 30-04-2025

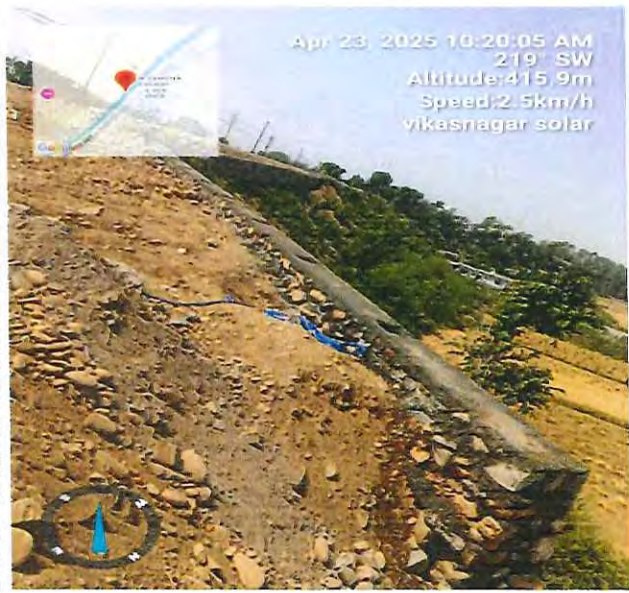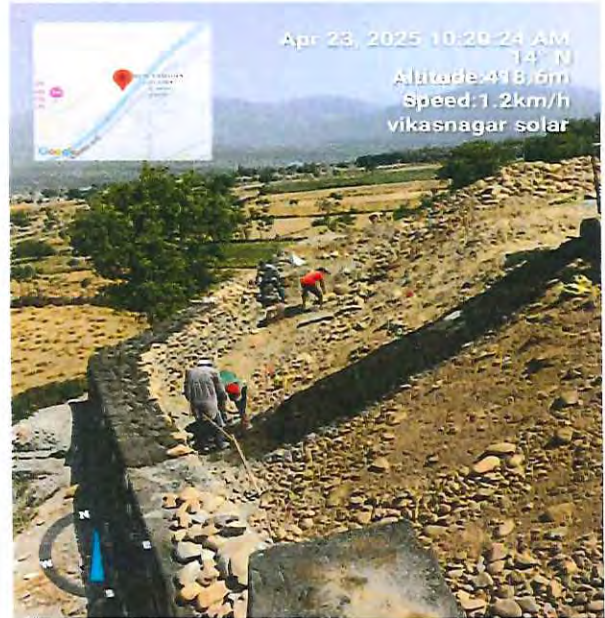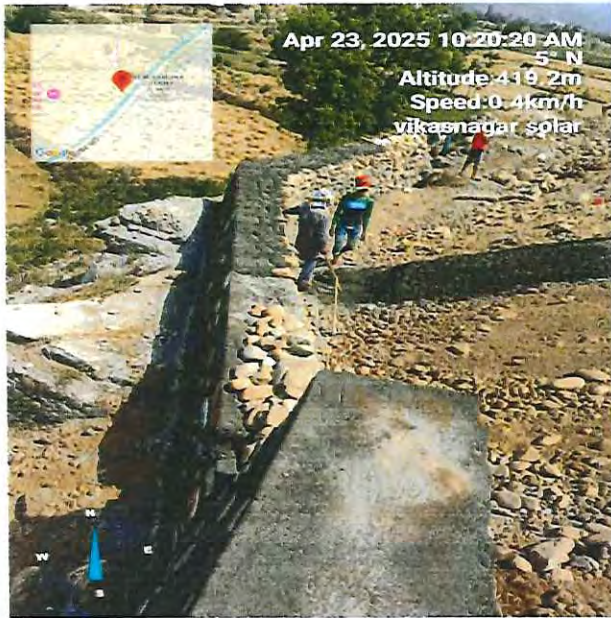

Annexure-I (Work Progress Photos)

Site Name: 2.5 MW Canal Bank Solar PV Plant (UJVNL Project, Dakpathar, Uttarakhand)




Work Progress Report: 16-04-2025 to 30-04-2025



Annexure-I (Work Progress Photos)

Site Name: 2.5 MW Canal Bank Solar PV Plant (UJVNL Project, Dakpathar, Uttarakhand)


Work Progress Report: 01-05-2025 to 03-06-2025

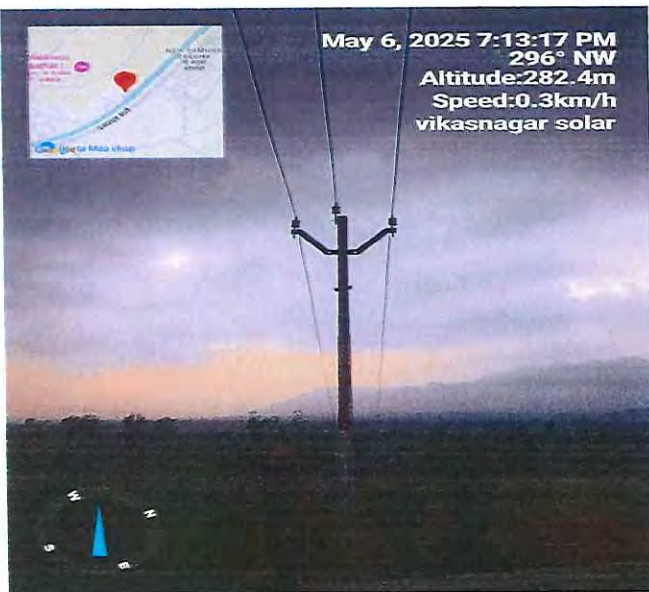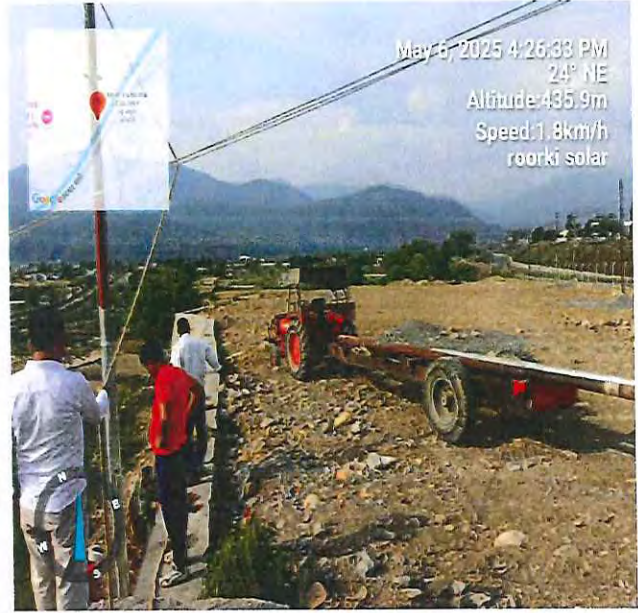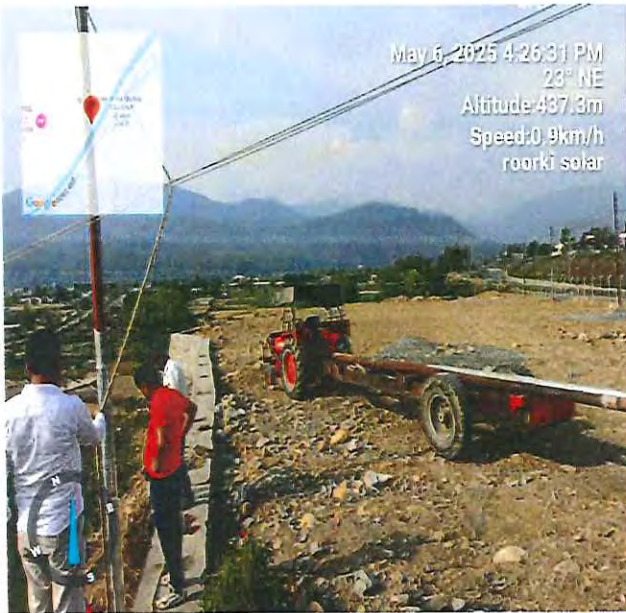

Annexure-I (Work Progress Photos)

Site Name: 2.5 MW Canal Bank Solar PV Plant (UJVNL Project, Dakpathar, Uttarakhand)

Work Progress Report: 16-04-2025 to 30-04-2025

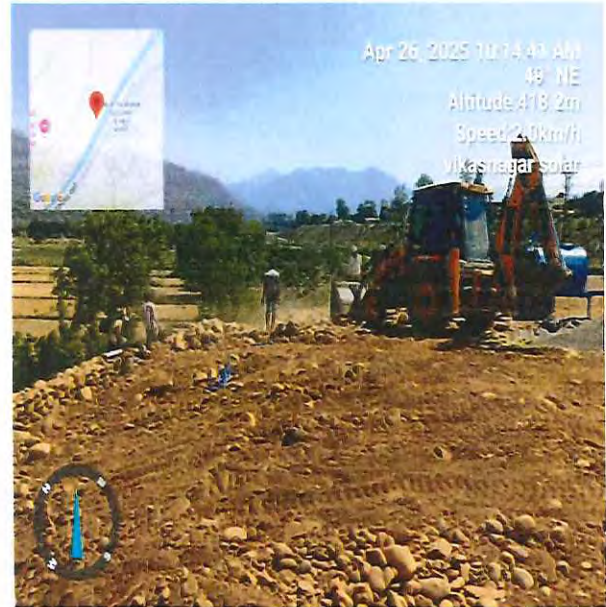


26-04-2025



Annexure-I (Work Progress Photos)

Site Name: 2.5 MW Canal Bank Solar PV Plant (UJVNL Project, Dakpathar, Uttarakhand)

Work Progress Report: 01-05-2025 to 03-06-2025

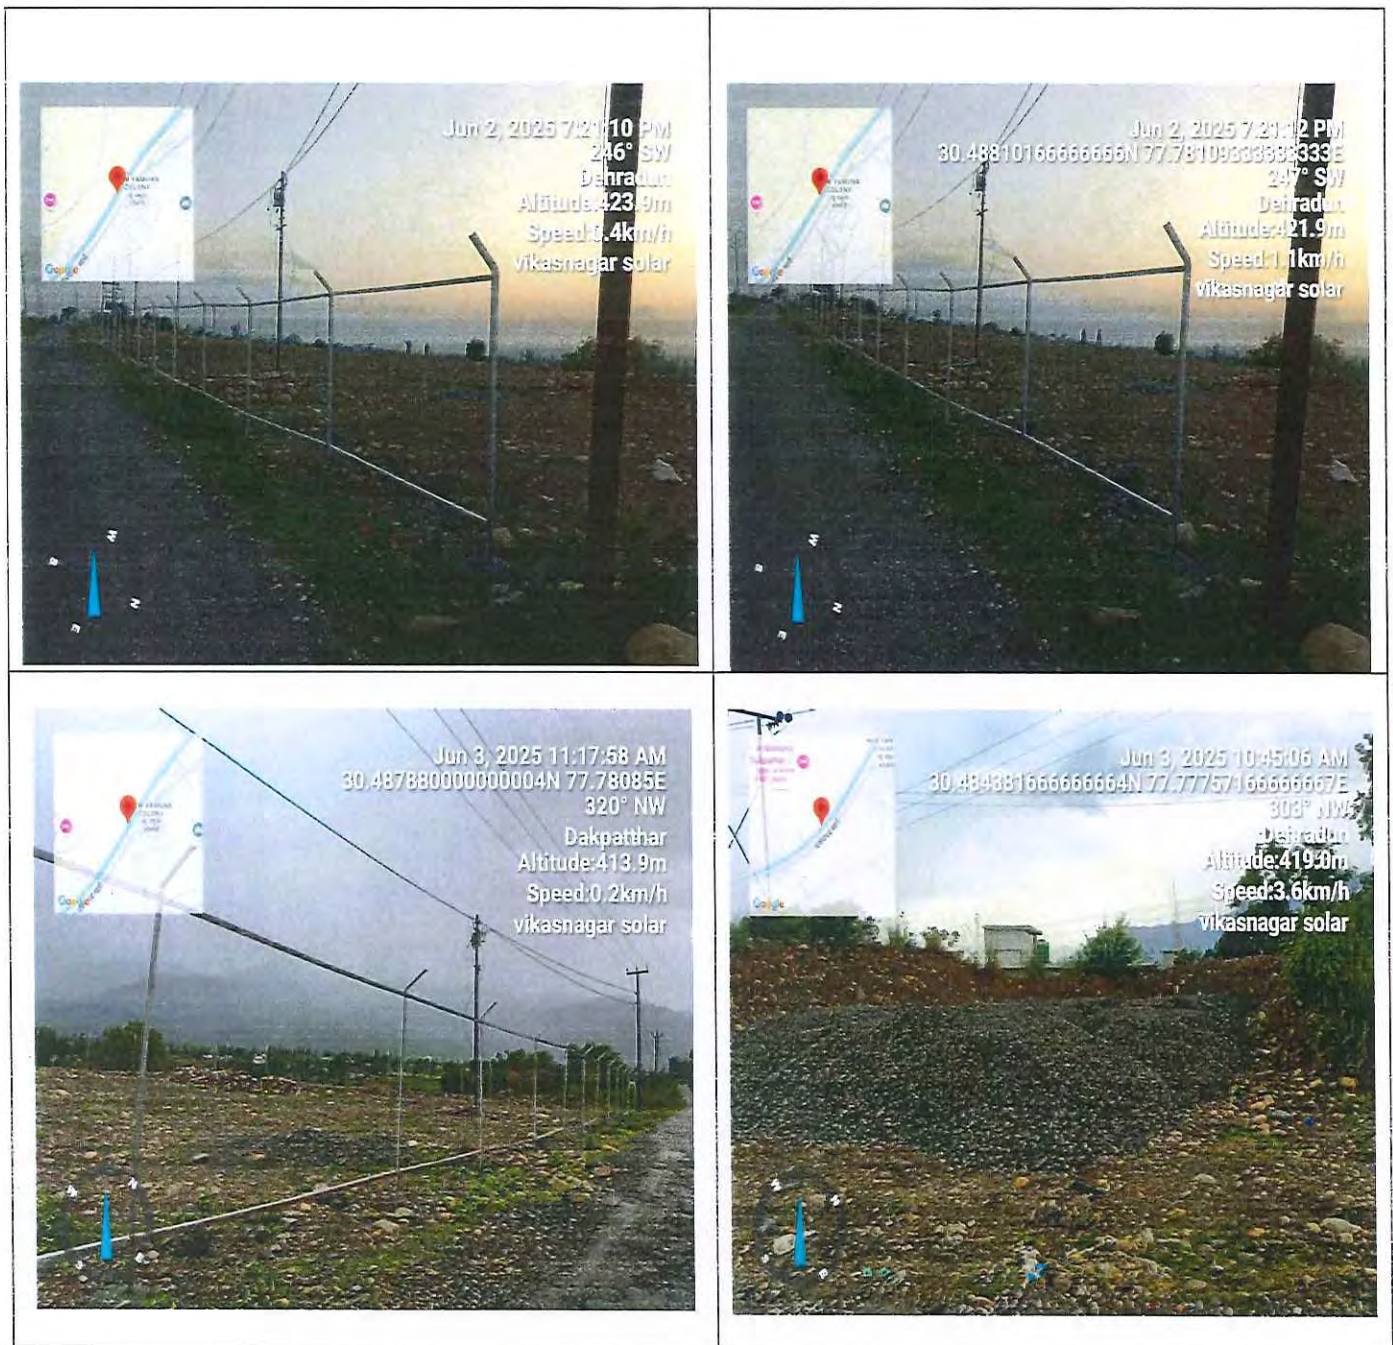

Annexure-I (Work Progress Photos)

Site Name: 2.5 MW Canal Bank Solar PV Plant (UJVNL Project, Dakpathar, Uttarakhand)

Work Progress Report: 01-05-2025 to 03-06-2025



पत्रांक: 84 / यूजेवीएन लि० / अधि.अभि.(सोलर) /

दिनांक: 05-04-2025

विषय- डाकपत्थर शक्तिनहर के पुल नं०-01 के समीप लग रहे 2.5 मे०वा० सौर संयंत्र में पुलिस सुरक्षा उपलब्ध कराये जाने के सम्बन्ध में।


उपजिलाधिकारी
विकास नगर, देहरादून।

महोदय कृपया उपरोक्त विषयक अवगत कराना है कि उत्तराखण्ड सरकार की महत्वाकांक्षी 2.5 मे०वा० सौर संयंत्र परियोजना की स्थापना हेतु यूजेवीएन लि० के माध्यम से मै० इवाल्व ग्रीन एनर्जी प्रा० लि० सौर विकासकर्ता द्वारा संपादित किया जा रहा है। वर्तमान में भूमि के समतलीकरण का कार्य किया जा रहा है। प्रस्तावित सौर भूमि पर वहां पर स्थित अतिक्रमण व्यक्तियों द्वारा बार-बार कार्य में व्यवधान उत्पन्न किया जा रहा है। जिसके कारण उक्त सौर संयंत्र लगाने में विलम्ब हो रहा है।

सौर विकासकर्ता द्वारा कार्य कर रहे कर्मचारियों की सुरक्षा किये जाने एवं बार-बार कार्य में व्यवधान उत्पन्न न हो, के लिए सौर विकासकर्ता द्वारा पुलिस बल की मांग की गयी है। (प्रतिलिपि संलग्न)।

अतः उक्त के सम्बन्ध में आपसे निवेदन है कि उक्त 2.5 मे०वा० सौर संयंत्र परियोजना को ससमय सम्पन्न कराये जाने के क्रम में, भूमि समतलीकरण कार्य किये जाने के दौरान डाकपत्थर शक्तिनहर के पुल-01 के समीप पुलिस बल की व्यवस्था करवाये जाने का कष्ट करें।

संलग्नक: यथोपरि।


(एस.एन. प्रजापति)
अधिकांश अभियन्ता (सोलर)

प्रतिलिपि:-

1. उपमहाप्रबन्धक(सोलर,एम०एम०एण्ड सी०एम०), यूजेवीएन लि०, गंगा भवन, यमना कालोनी, देहरादून।
2. अधिकांश अभियन्ता (जानपद), यूजेवीएन लि०, ढालीपुर, देहरादून को सूचनार्थ एवं आवश्यक कार्यवाही हेतु प्रेषित।
3. मै० इवाल्व ग्रीन एनर्जी प्रा० लि० को इस आशय से प्रेषित कि कृपया उपजिलाधिकारी कार्यालय से समन्वय स्थापित कर कार्य को अतिशीघ्र पूर्ण करने का कष्ट करें।



UJVNL LIMITED

(A Govt. of Uttarakhand Enterprise)

मुख्य कार्यालय (मुख्य) : देवी, नैनीताल, उत्तराखण्ड 249006 (देवी, नैनीताल, उत्तराखण्ड)।
Office of the Executive Engineer (Solar), "U Jivul", Moharani Bagh, G.M.S. Road, Dehradun 249006 (Uttarakhand).
CIN No. 401011CR2001SGC025866
ISO 9001:2015, ISO 14001:2015 & 45001:2017 Certified

No. 82 /UJVNL/EE (Solar)/

Date: 05-04-2025

Subject: Request for Tree cutting & Clearance- 2.5 MW Canal Bank Solar PV Project, Dakpathar, Dehradun.

Executive Engineer (Civil)


UJVNL Ltd.

Dhalipur, Dehradun.


Please find enclosed herewith the letter No. SEPL/TRPR/UJVNL/2.5 MW/TR-16. Dated: 03.04.2025 of M/s Evolve Green Energy Pvt.Ltd, Chennai, requesting for tree clearance.

In this regard, please do needful for removal of tree under site of 2.5 MW Canal Bank Solar PV Plant near bridge no-1 Dakpathar on Urgent Basis so that Plant can be installed in time.

Encl: As Above


(S. N. Prajapati)
Executive Engineer (Solar)

Cc: M/s Evolve Green Energies Private Limited, Chennai with request to co-ordinate with Civil Officials for early action.



(सहस्रायुष्मन्त सरकारी का समकर्म)

UJVNL Limited


A Govt. of Uttarakhand Enterprise

Office of Executive Engineer, Project Cell Maintenance, Dhalpur (Dehradun)- 248 147
PIN No. 2481011-R20015670-0258666अधिशारी अभियन्ता (सोलर),
यूजेवीएन लिमिटेड, गंगा भवन,
जीएमएरा रोड, देहरादून।

विषय:- सोलर प्लाण्ट निर्माण कार्य स्थल पर सिल्ट/मिट्टी आदि कटान के सम्बन्ध में।

कृपया उपरोक्त विषयक अवगत कराना है कि यूजेवीएन लिमिटेड की भूमि पर किये गये अतिक्रमण को अतिक्रमण से मुक्त कर भूमि को सौर ऊर्जा सयंत्र स्थापित करने हेतु आपके कार्यालय को हस्तान्तरित की गयी है। जिसमें सोलर सयंत्र स्थापित किये जाने का कार्य किया जा रहा है। इसके अतिरिक्त सौर सयंत्र स्थापन हेतु समतलीकरण एवं स्थल पर सर्वेक्षण का कार्य भी आपके कार्यालय के अन्तर्गत किया जा रहा है। सोलर सयंत्र स्थापित किये जाने वाले स्थलों की मिट्टी का समतलीकरण (Leveling Dressing) के दौरान स्थल की सिल्ट/मिट्टी इत्यादि काटकर अन्यत्र स्थापित न किया जाय। यदि आवश्यक हो तो सोलर प्लाण्ट कार्य स्थलों से मिट्टी आदि सागरी का कटान कर अन्यत्र स्थापित करने हेतु उपजिलाधिकारी महोदय एवं प्रशासन से स्वीकृति लेना वांछनीय है।

अतः उपरोक्तानुसार सोलर सयंत्र स्थापन हेतु कार्य स्थल पर सिल्ट/मिट्टी इत्यादि के निस्तारण हेतु अपने कार्यालय स्तर से कार्यवाही करने का कष्ट करें।


8/03/2025
(गिरिश चन्द्र जोशी)
अधिशारी अभियन्ता

प्रतिलिपि निम्नलिखित को सूचनार्थ एवं आवश्यक कार्यवाही हेतु प्रेषित।

1. अधिशारी निदेशक (जानपद), लखवाड़ व्याप्ती परियोजना, डाकमत्थर, देहरादून।
2. महाप्रबन्धक (जानपद अनुरक्षण), यूजेवीएन लिमिटेड, गंगा भवन, यमुना कालोनी देहरादून।
3. उपमहाप्रबन्धक (सोलर) यूजेवीएन लि. गंगा भवन, यमुना कालोनी देहरादून।
4. उपमहाप्रबन्धक (जानपद अनुरक्षण) यूजेवीएन लि. ढालीपुर, देहरादून।
5. सहायक अभियन्ता, प.जा.अ. ढालीपुर देहरादून।

To,
M/c. SHIMATO ENTERPRISES, Pvt Ltd.
Chennai.

कृपया समतलीकरण के दौरान स्थल की सिल्ट/मिट्टी इत्यादि काटकर अन्यत्र स्थापित न किया जाय। सिल्ट/मिट्टी का उपयोग केवल दोनो साइटों के समतलीकरण में किया जाय। इसके अतिरिक्त निम्नलिखित समतलीकरण ध्यानपूर्वक एवं सुरक्षित रूप से निरूपित किया जाय।
सूचनार्थ एवं आवश्यक कार्यवाही हेतु प्रेषित।

- 1- अधिशारी अभियन्ता (जानपद), ढालीपुर, यूजेवीएन लिमिटेड
- 2- सहायक अभियन्ता (सोलर) को 31/03/2025

31/03/25
UJVNL Limited
"UJVN" GMS Road
Dehradun-248101

No: 51/UJVNL/EE(Solar) | Dated: 10/03/2025

evolve

CHENNAI · DELHI · MUMBAI · AHMEDABAD
COIMBATORE · SRI LANKA · HONG KONG

Office No. 471, MIDC Industrial Estate
(B) Ambur, Chennai - 601006
www.evolveindia.in
info@evolveindia.in
044-4210 6640

Ref No: SEPL/TRPR/UJVNL/2.5MW/TR-08

07-03-2025

To,
The Executive Engineer (Solar),
UJVNL Limited,
"Ujjwal", Maharani Bagh,
GMS Road, Dehradun-248006.

Subject: Request for Tree Cutting & Clearance – 2.5 MW Canal Bank Solar PV Project, Dakpathar, Dehradun

Respected Sir,

With reference to LOI No: B-51/UJVNL/EE (Solar) dated 17.02.2024 and the subsequent Power Purchase Agreement (PPA) signed on 7th August 2024 for the 2.5 MW Canal Bank Grid-Connected Solar PV Plant on Yamuna Power Channel near Bridge No-1, Dakpathar, District Dehradun, Uttarakhand.

We kindly seek your urgent support in cutting and clearing the trees on both sides of the canal bank. A total of 318 trees are present at the site, which need to be cleared to enable the commencement of project construction activities. We have enclosed the detailed tree list for your reference.

We seek your immediate attention to this matter, as it will help us proceed with the planned schedule.

Thank you for your time and consideration. We look forward to your positive response.

For Shimato Enterprises Private Limited,

EE (CIVIL), UJVNL, Dehradun



Authorized Signatory

Enclosed: Detailed Tree List

Please after joint inspection, above mentioned trees are required to removed on urgent basis and as early as possible. It is therefore take necessary action on urgent basis.

SHIMATO ENTERPRISES PRIVATE LIMITED

AN ISO 9001:2015, 14001:2015, & OHSAS 18001:2007 CERTIFIED COMPANY. NSIC & DSI / MSME Registered Company

GSTIN: 33AAPCS2173L1ZZ

CC/M/s Shimato Enterprises Pvt Ltd for UJVNL Limited
necessity action

For: E.E. (Solar)
UJVNL Limited
"Ujjwal", Maharani Bagh,
GMS Road, Dehradun-248006

② AE (Solar) for n.d.

No: 50/UJVNL/EE (Solar) Dated: 10/03/2025

Detailed Tree List:

Sl. No.	Material	Quantity	Unit	Price	Amount	Rate
1	UKL	5		540.00	2700.00	540.00
2	UKL	10		50.70	507.00	50.70
3	UKL	8		80.90	647.20	80.90
4	UKL	24		90.100	2162.40	90.100
5	UKL	10		1.20 to 1.40	1200.00	120.00
6	UKL	5		1.20 to 1.40	600.00	120.00
7	UKL	11		1.50 to 1.60	1650.00	150.00
8	UKL	4		1.50 to 1.60	600.00	150.00
9	UKL	2		1.8 to 2.00	360.00	180.00
10	Silver	18		0.80 to 1.00	1800.00	100.00
11	Silver	34		1-1.2	3400.00	100.00
12	Silver	1		1.20 to 1.40	120.00	120.00
13	Silver	1		1.5-2	150.00	150.00
14	Kukat	18		0.40 to 0.50	720.00	40.00
15	Kukat	8		0.80 to 0.90	720.00	90.00
16	Kukat	5		1.00 to 1.40	500.00	100.00
17	Jakrenda	11		0.80 to 0.90	990.00	90.00
18	Jakrenda	11		0.90 to 1.20	990.00	90.00
19	Jakrenda	4		1.20 to 1.50	480.00	120.00
20	Jakrenda	1		1.5 to 1.8	150.00	150.00
21	Baken	3		0.20 to 0.25	60.00	20.00
22	Baken	33		0.30 to 0.40	990.00	30.00
23	Baken	9		0.60 to 0.70	540.00	60.00
24	shisham	4		0.20 to 0.30	120.00	30.00
25	shisham	3		0.40 to 0.50	120.00	40.00
26	shisham	5		0.60 to 0.70	300.00	60.00
27	shisham	3		1.20 to 1.30	360.00	120.00
28	kathal	4		0.30 to 0.40	120.00	30.00
29	Siris	5		0.60 to 0.70	300.00	60.00
30	Siris	4		1.00 to 1.20	480.00	120.00
31	Semal	1		0.50 to 0.60	60.00	60.00
32	Semal	1		1.20 to 1.30	120.00	120.00
33	Tun	1		1.20 to 1.30	120.00	120.00
34	Aam	6		0.50 to 0.60	300.00	50.00
35	Aam	4		0.80 to 1.00	320.00	80.00
36	Aam	1		0.90 to 1.00	90.00	90.00
37	Uthi	1		30 to 40	30.00	30.00
38	Amrud	5		0.20 to 0.30	150.00	30.00
39	Amrud	6		0.30 to 0.40	180.00	30.00
40	Jamun	1		0.30 to 0.40	120.00	120.00
41	Jamun	3		0.60 to 0.70	180.00	60.00
42	Amaltas	3		0.50 to 1.00	150.00	50.00
43	Gulet	1		1.20 to 1.40	120.00	120.00
44	Gulet	2		1.40 to 1.80	280.00	140.00
45	Gulet	1		1.00 to 1.20	100.00	100.00
46	Gular	1				
					Total	745057.15

SHIMATO ENTERPRISES PRIVATE LIMITED

AN ISO 9001:2015, 14001:2015, & OHSAS 18001:2007 CERTIFIED COMPANY, NSIC & SSI / MSME Registered Company.

GSTIN: 33AAPCS2173L1ZZ



यूजीवएन लिमिटेड

(उत्तराखण्ड सरकार का उपक्रम)

UJVNL LIMITED

(A Govt. of Uttarakhand Enterprise)

कार्यालय-अधिशायी अभियन्ता (सोलर), "उज्ज्वल", महारानी बाग, जीएमएस रोड, देहरादून-248006 (उत्तराखण्ड), दूरभाष: 0135-2761484, फैक्स: 0135-2763506
Office of the Executive Engineer (Solar), "Ujjwal", Maharani Bagh, G.M.S. Road, Dehradun-248006 (Uttarakhand), Phone: 0135-2761484, Fax: 0135-2763506
CIN No. 40101UR2001SGC025866

ISO 9001:2015, ISO 14001:2015 & 45001:2017 Certified

Date: 26-12-2024

Subject:- Regarding Tree cutting approval in land of 2.5 MW Canal Bank Solar PV Plant at Bridge no-1 Dakpathar.

Executive Engineer (Civil)
Dhalipur.
Dehradun.

Please find attachment the Solar Developer M/s Shimato Enterprises Pvt. Ltd. request letter No. NIL, dated: 24.12.2024 vide which request to removal of tree for clearing the land for construction.

It is therefore requested to do needful for felling of tree in both sides North & South portion at the earliest so that Solar developer start the work.

Encl: As above.

Signed by
Shyam Narayan Prajapati
Date: 26-12-2024 13:31:17
(S.N. Prajapati)
Executive Engineer (Solar)

Cc:

1. M/s Shimato Enterprises Private Ltd. with request to co-ordinate the Civil Officials, UJVNL Dhalipur for early action.
2. Assistant Engineer (Solar), UJVNL for necessary action.
